




Clermont County Transportation Improvement District

September 13, 2024


Round Bottom Road Bridge Replacement (C106-3.03)

- Construction may start this fall, waiting on pre-con
- Estimated completion – Early May, 2025

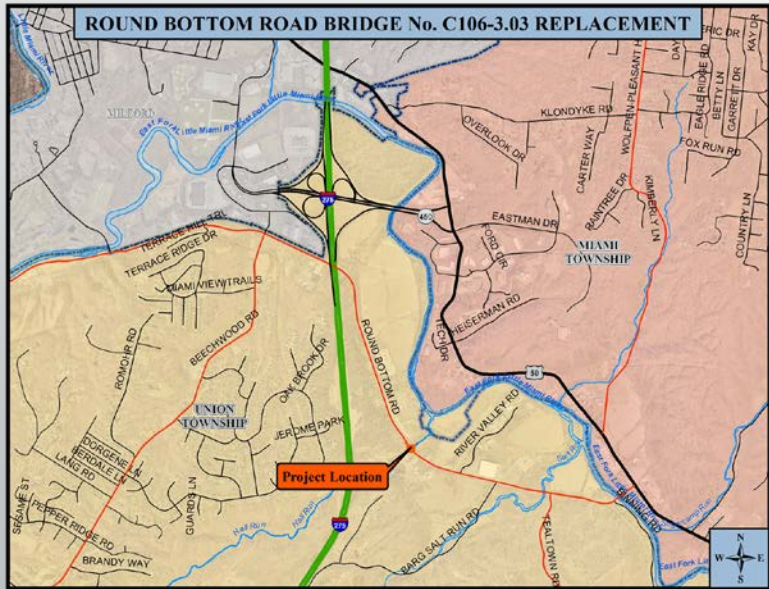


East Loveland Bridge Replacement (M01-0.18)

- Majority of bridge work is complete, few minor railing issues to complete
- One lane is still supposed to happen within the next few weeks while crews continue to widen the road and install Sanitary lines.

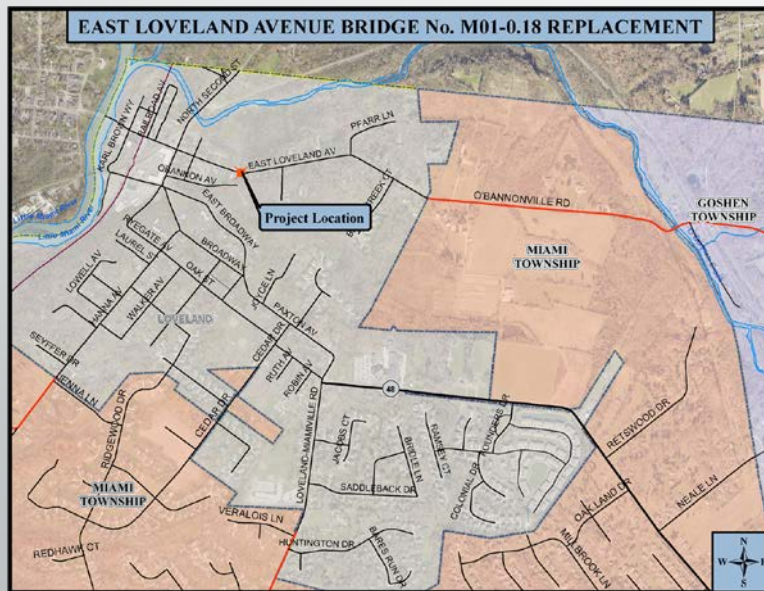


Aicholtz Road Roundabouts

- Work south and west of RAB #3 is done
- Working on RAB #3 to the end of project towards Clepper

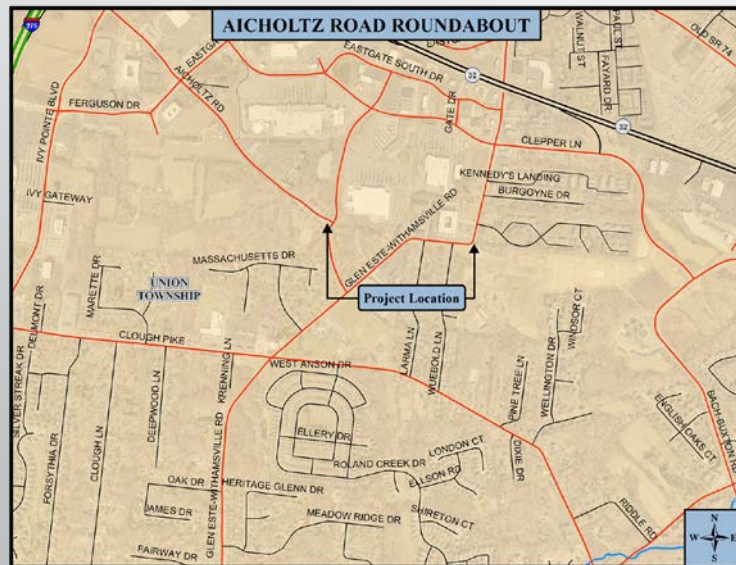


Bach-Buxton Road Roundabouts

- OKI recommended \$2.8M of \$3.3M requested
- Final approval of STBG funds in October

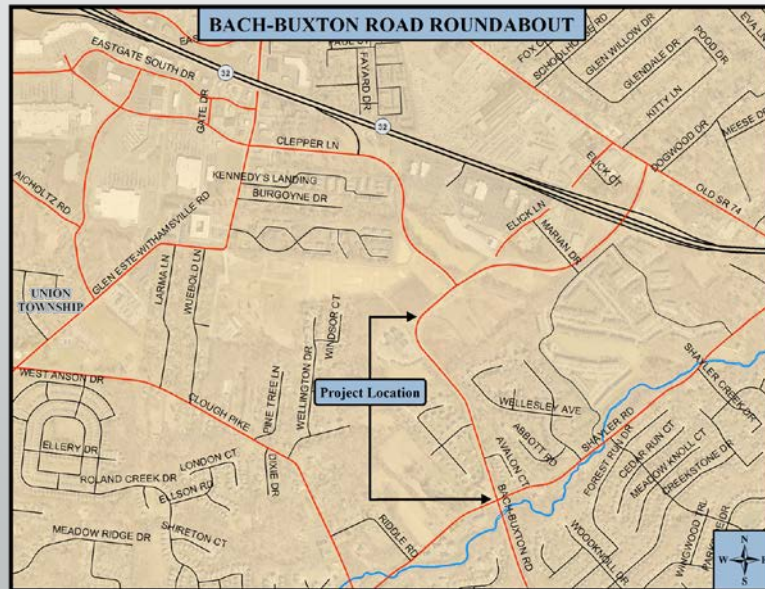


Deerfield Road and Woodville Pike Roundabouts

- ODOT Comments received - Finalizing public involvement materials
- 2028 Construction

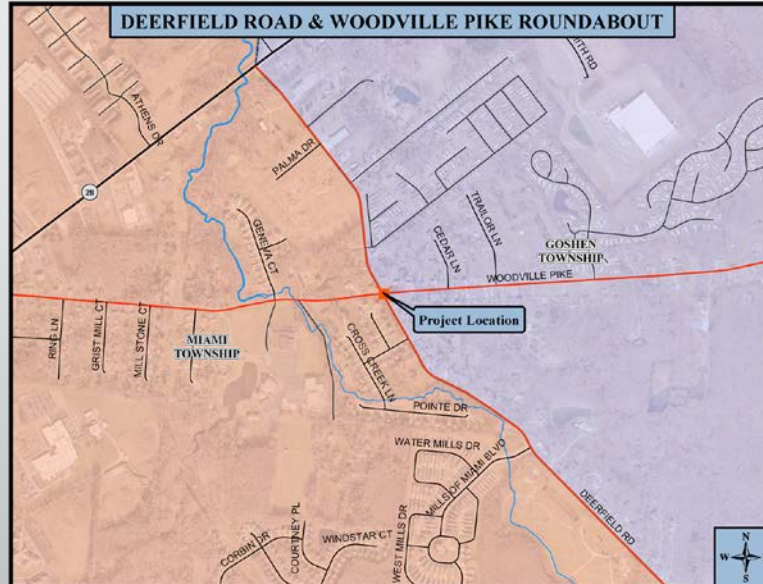


Glancy Corner-Marathon Road Bridge Rehabilitation (C54-2.16)

- Design under contract with Burgess & Niple
- Stage 1 plans submitted to ODOT in June, comments by end of month

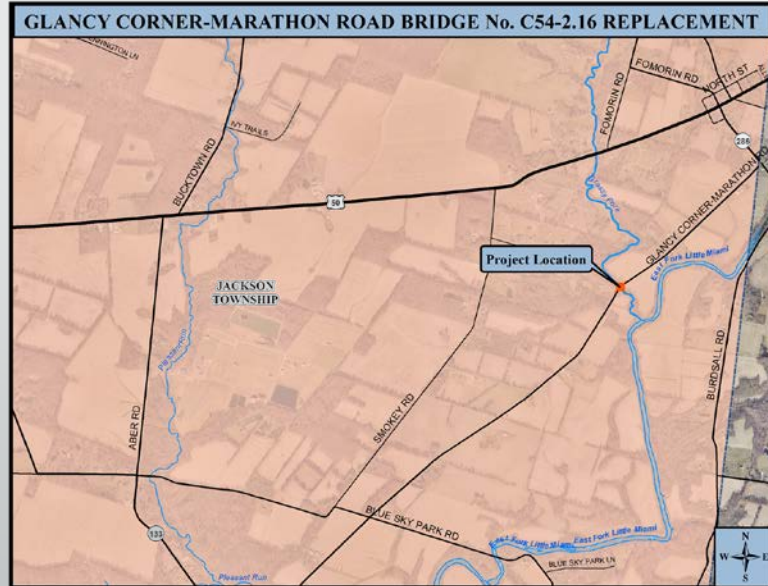

Ireton Trees Road Bridge Replacement (T39-1.20)

- Under contract with KT Holden
- Work starting on September 30th
- Closed the road last week due to rapid deterioration of the beams
- County crews working on berming

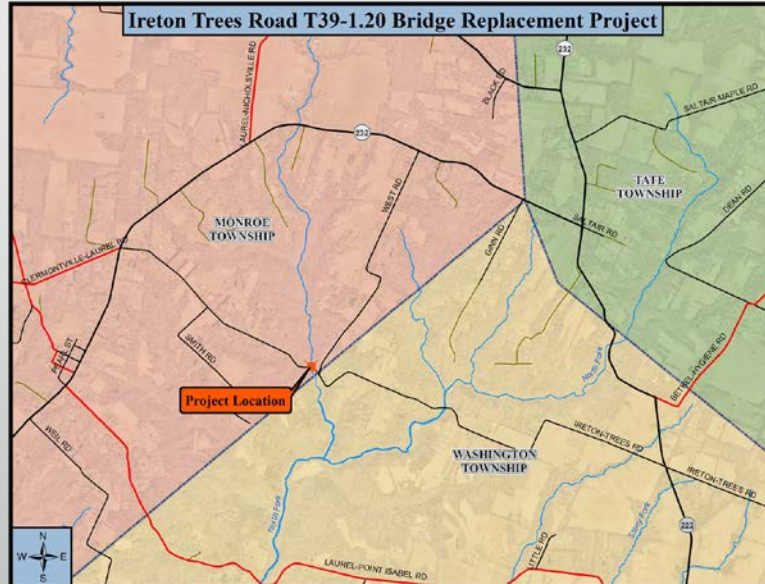


US 50/SR 132 Intersection Improvements Project

- Western Intersection
 - Opened under temporary configuration
- Eastern Intersection
 - Finishing storm and water lines
 - Widening in progress
- Complete by end of 2024




Felicity Cedron Road Bridge Rehabilitation Project (C45-2.45)

- Just finished survey work, will get that to Stantec
- FY26 Construction

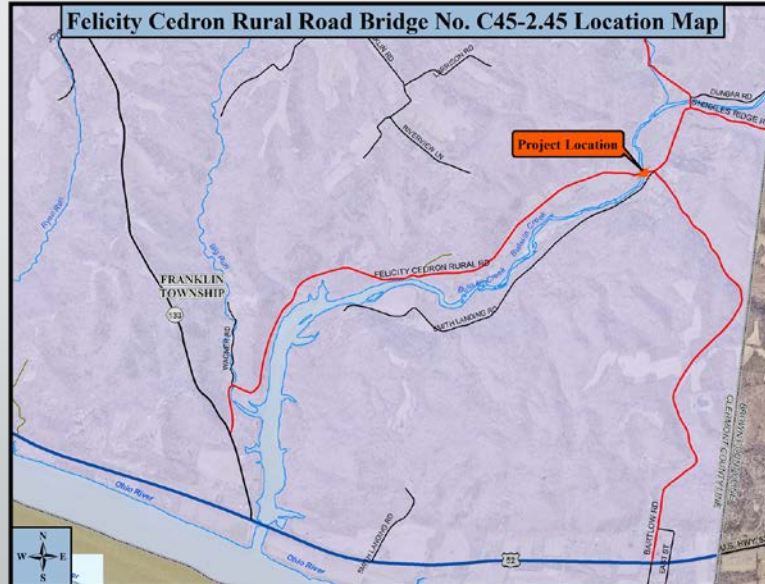


Champion's Way Roadway Improvement

- Under Construction. Majority of storm is finished, working on getting roadway filled to grade.
- Pouring curb and possibly asphalt next week

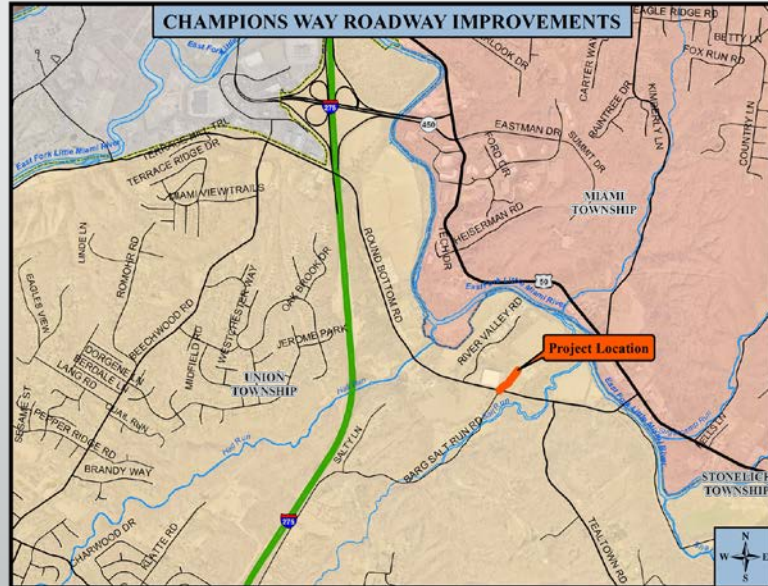

Neville-Penn Schoolhouse Landslide Repair

- Construction began August 27th
- Pier wall complete
- Installing guardrail, repairing pavement, etc.

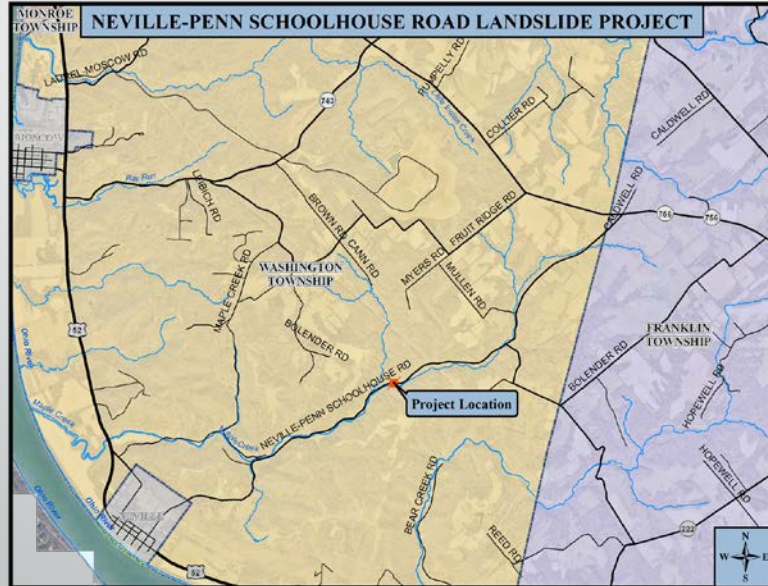

District Drive – Rise Way Roadway Project

- Pending Miami Township determination of funding

