




# Clermont County Transportation Improvement District

December 13, 2024

# Round Bottom Road Bridge Replacement (C106-3.03)

- Scheduling pre-con to establish construction dates
- Still waiting utility moves
- Completion Estimate— May, 2025

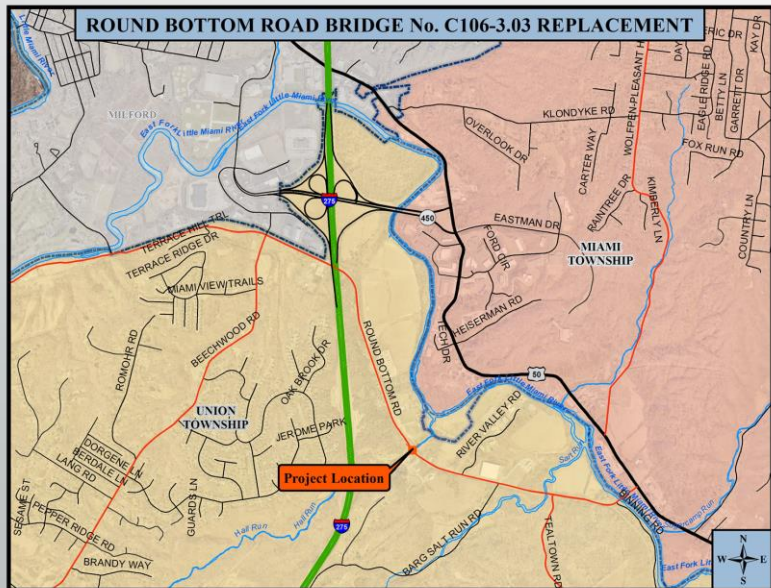

# East Loveland Bridge Replacement (M01-0.18)

- Project is Complete




# Aicholtz Road Roundabouts

- Project is now fully open to the public
- Finishing up signage, and minor punch list items




# Bach-Buxton Road Roundabouts

- Coordinate with Union Twp/Arcadis/OKI to combine projects & adjust schedule
- Scoping meeting for changes in early January

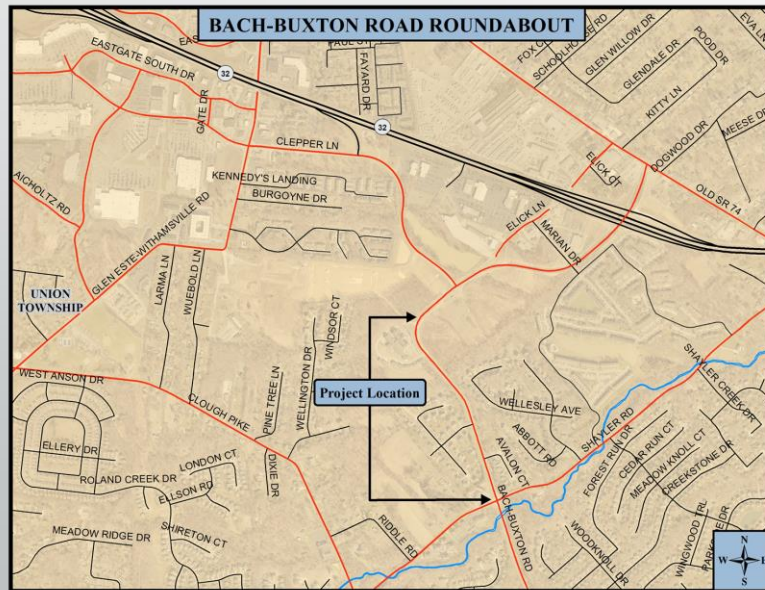


# Deerfield Road and Woodville Pike Roundabouts

- Public comment summarization
- Stage 1 plans under design
- 2028 Construction

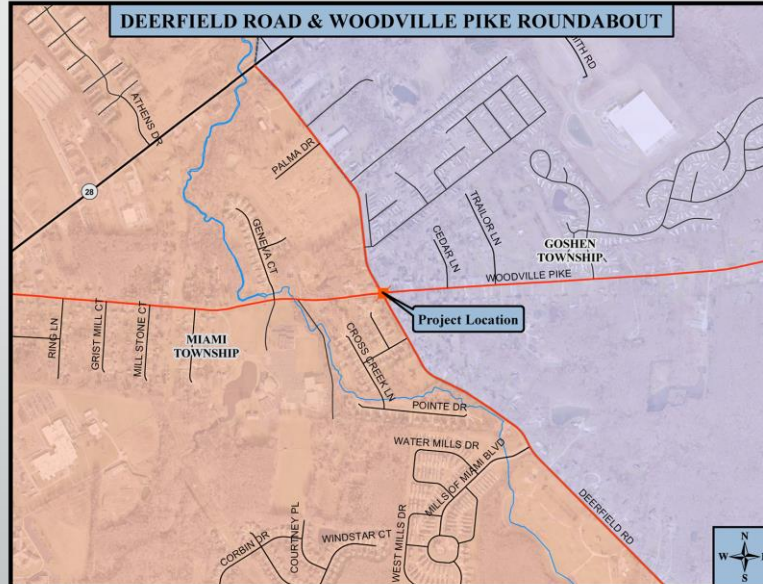

# Glancy Corner-Marathon Road Bridge Rehabilitation (C54-2.16)

- Received ODOT review in early October
- B&N has addressed ODOT review and has submitted stage 3 plans for review.

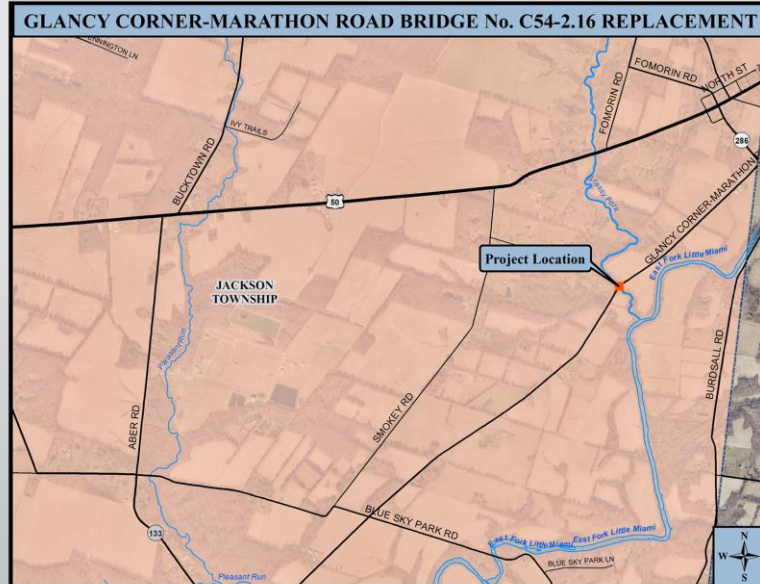


# Ireton Trees Road Bridge Replacement (T39-1.20)

- Project is completed with a few minor issues remaining, scheduled for final repairs today.




# US 50/SR 132 Intersection Improvements Project

- Work to be completed:
  - Complete signal installation
  - Final punch list items
- Complete in early 2025

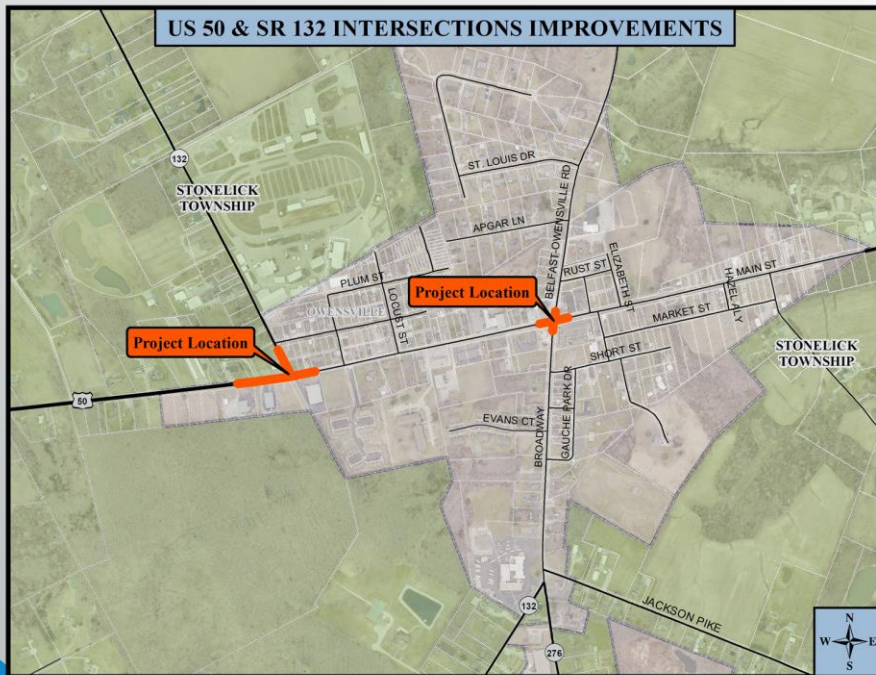

# Felicity Cedron Road Bridge Rehabilitation Project (C45-2.45)

- Stantec working on design
- FY26 Construction

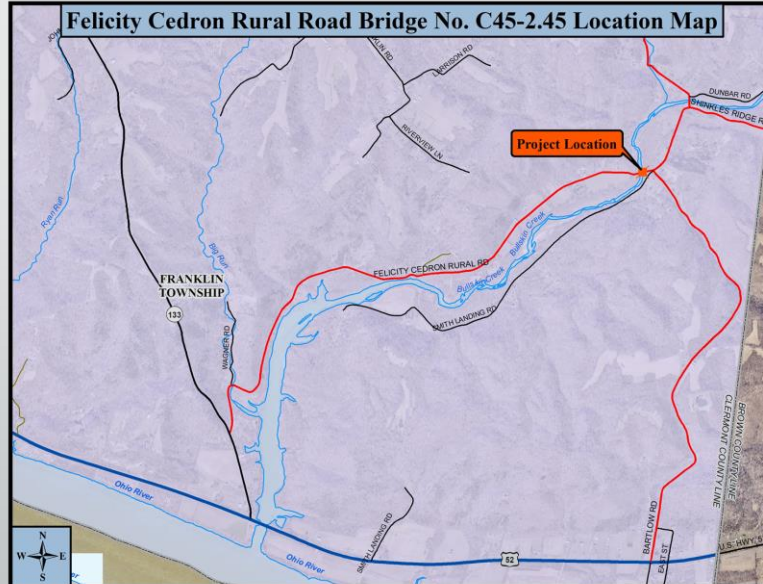



# Champion's Way Roadway Improvement

- Project is complete, working on final payments and closeout




# District Drive – Rise Way Roadway Project

- Pending Miami Township determination of funding

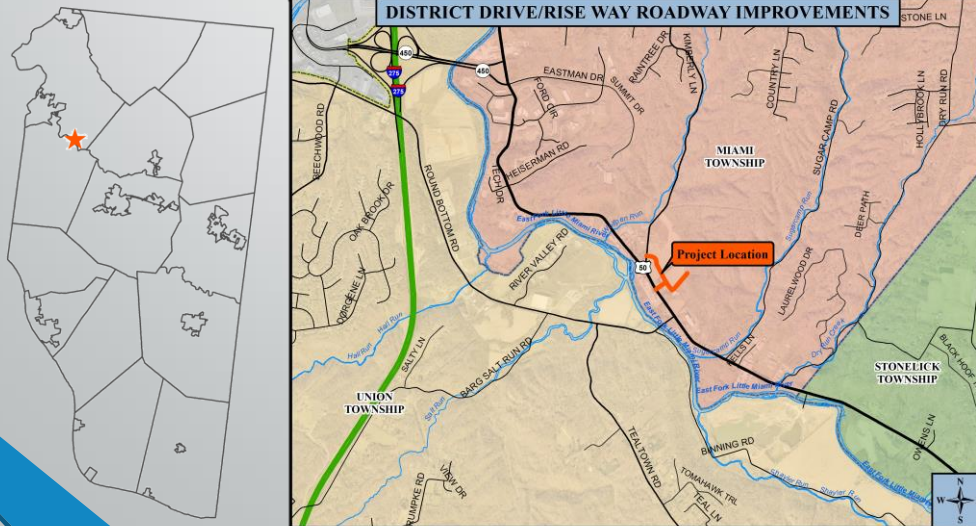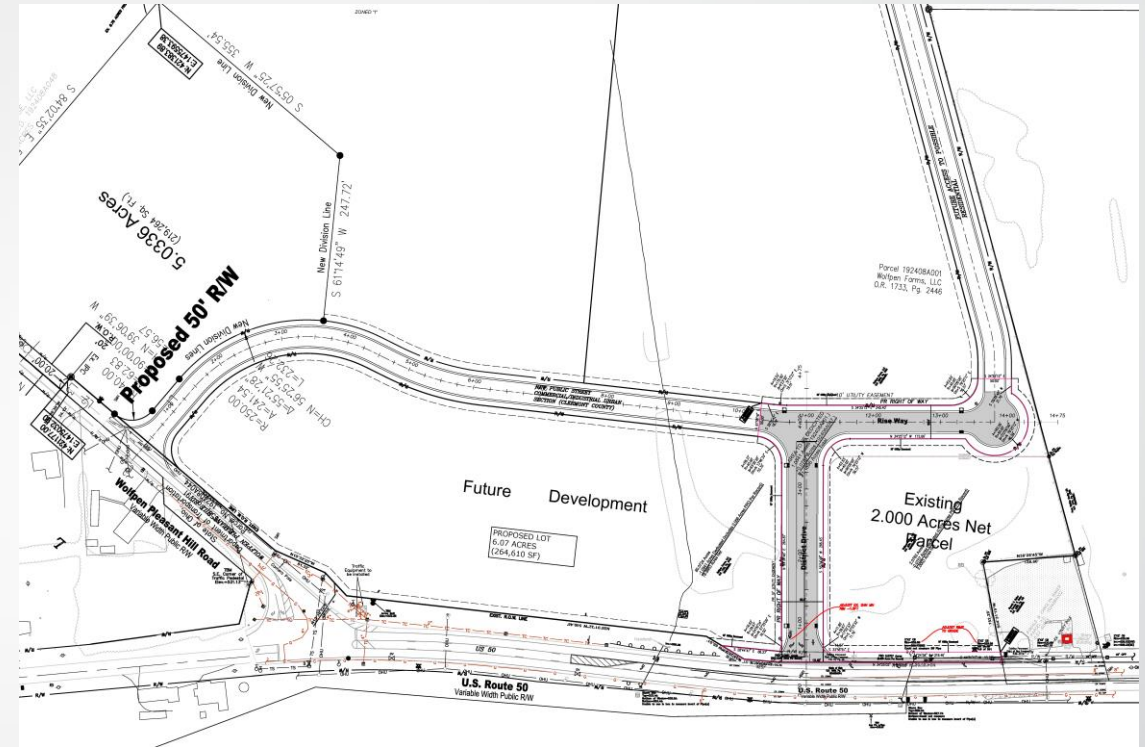

# Gibson Road Bridge Replacement (T194-1.30)

- Precon mtg next week for schedule and details.
- Completion estimate - 8/1/2025

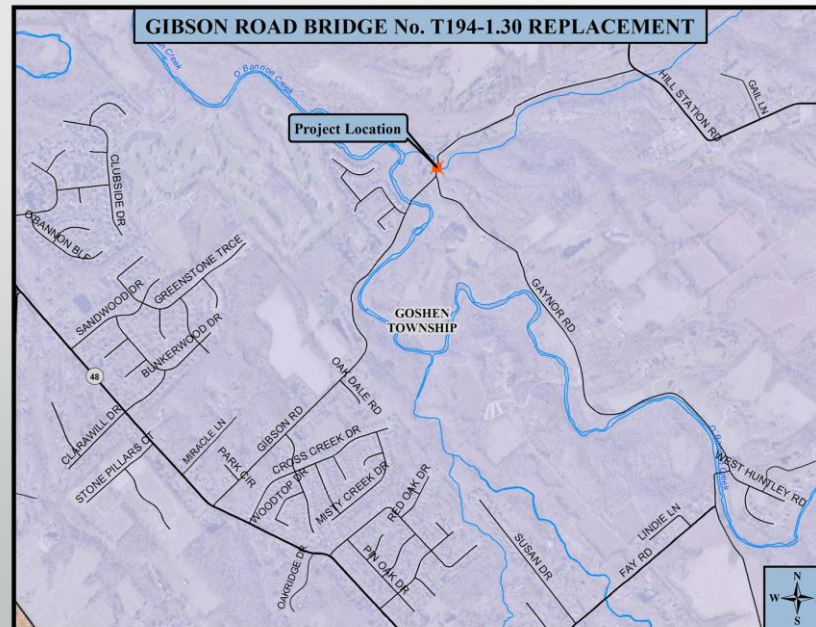


# Shiloh Road Bridge Replacement (C157-2.35)

- Precon mtg next week for schedule and details.
- Completion Estimate - 8/1/2025




# Bray Road Bridge Replacement (T170—1.27)

- Precon mtg next week for schedule and details.
- Work has already been started
- Completion Estimate - 8/1/2025

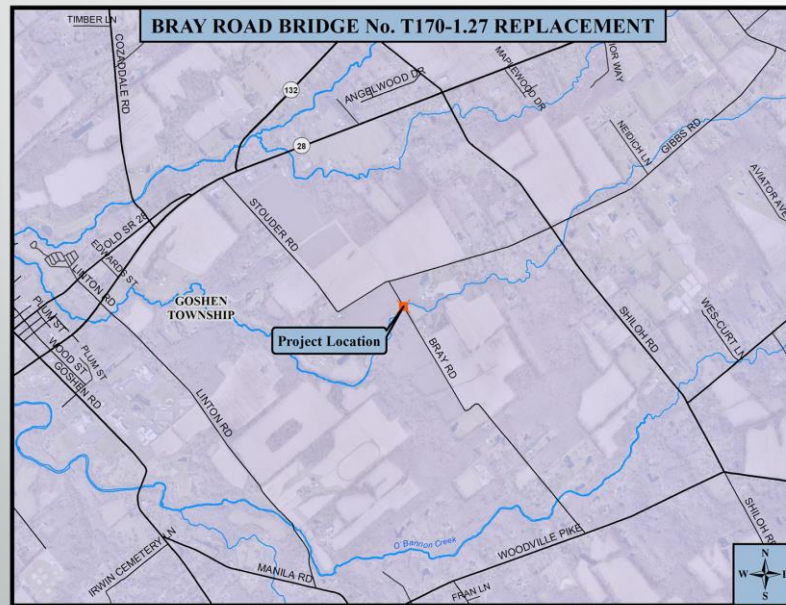

# Marathon Edenton Road Bridge Replacement (C82-1.61)

- Working on final drawings.
- Bid when drawings are complete and final ROW is acquired.

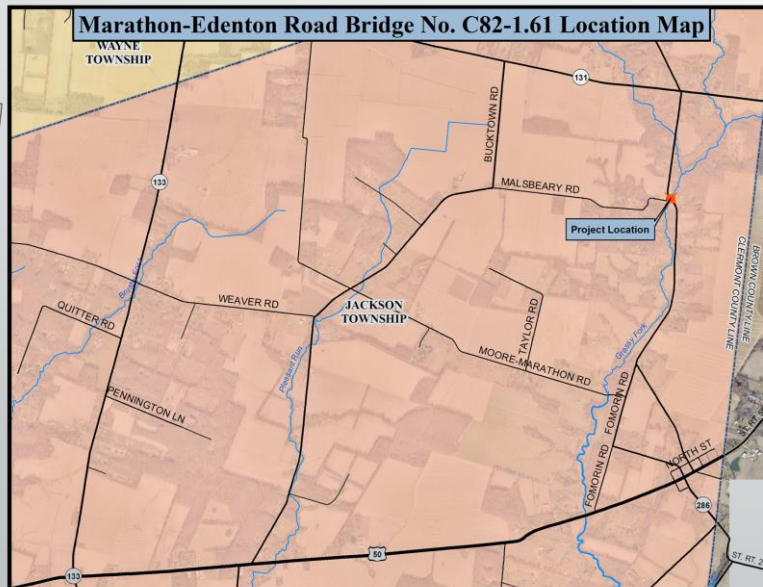

# Newtonsville Hutchinson Road Bridge Replacement (C93-2.08)

- Working on final ROW
- Bid project after ROW by end of 2024

