




# Clermont County Transportation Improvement District

February 18, 2025

# Round Bottom Road Bridge Replacement (C106-3.03)

- The watermain is installed and ready for testing - once it is approved, the bridge can be taken down and started
- Completion Estimate— May 2025

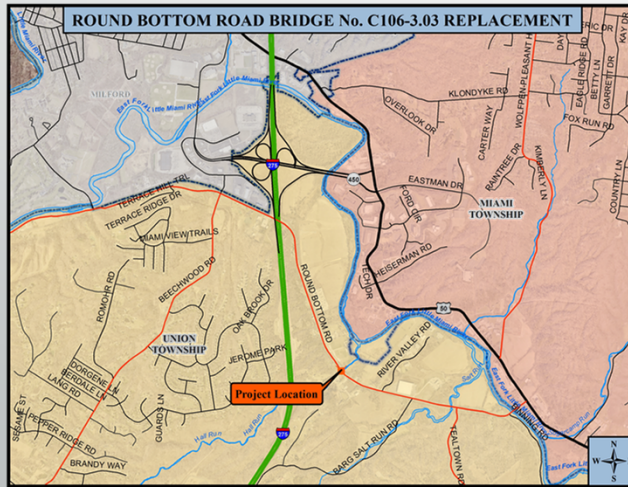


# Aicholtz Road Roundabouts

- Project is now fully open to the public
- Finishing up signage, and minor punch list items and final payments.





# Bach-Buxton Road Roundabouts

- Arcadis working Stage 1 plans - due in spring
- ODOT Scoping meeting being scheduled

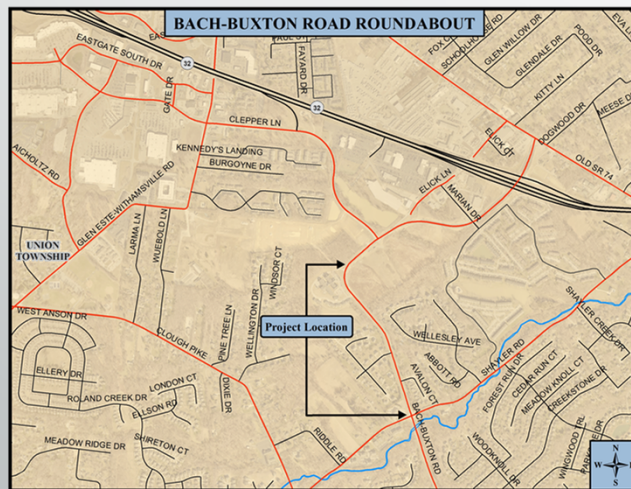


# Deerfield Road and Woodville Pike Roundabouts

- Public comment summarization sent
- ODOT comments received for Stage 1
- 2028 Construction

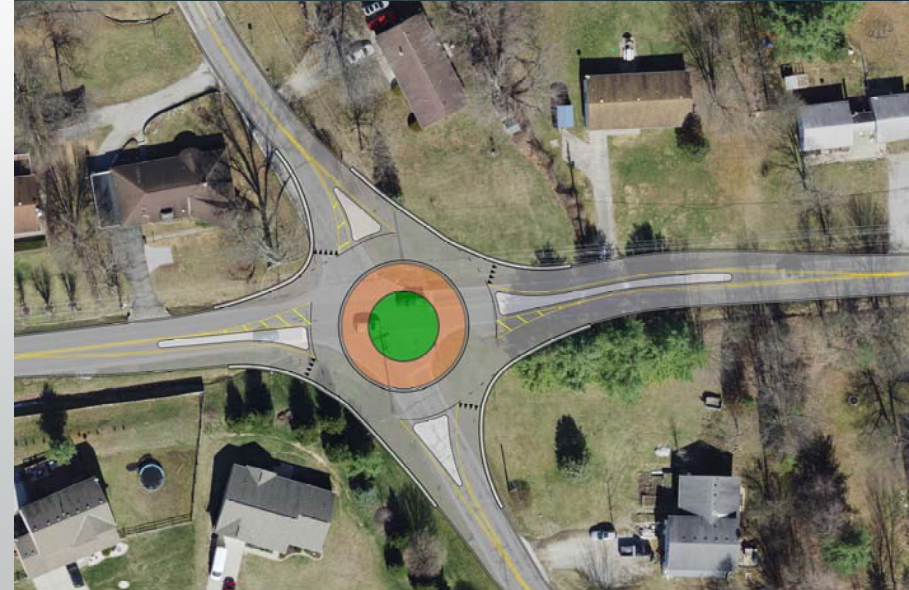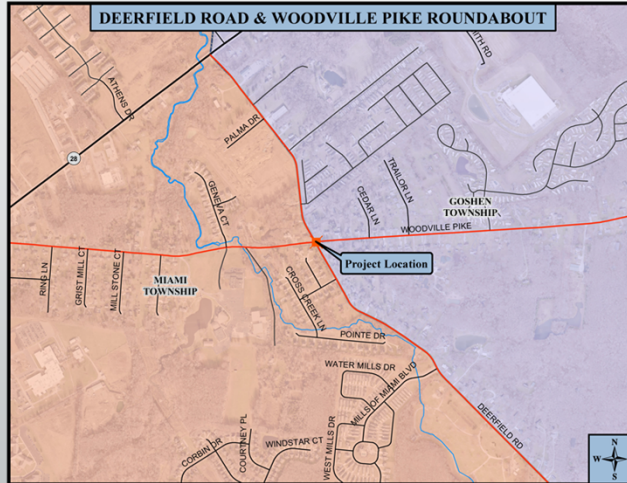

# Glancy Corner-Marathon Road Bridge Rehabilitation (C54-2.16)

- PS&E Package submitted to ODOT
- Bidding will probably be in March/April depending when we get FHWA authorization to proceed.

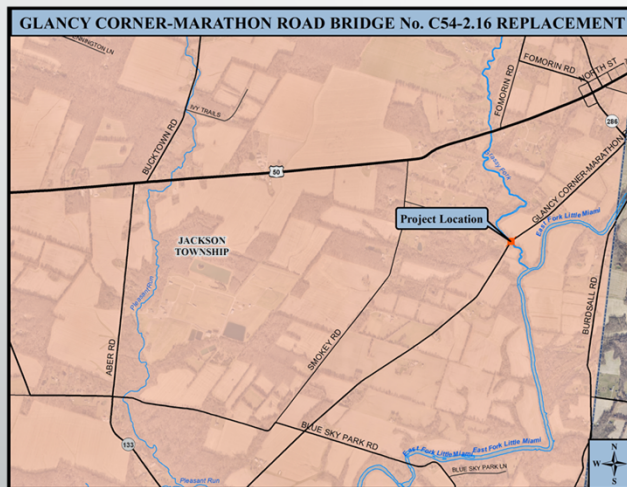


# Ireton Trees Road Bridge Replacement (T39-1.20)

- Project is completed, working on final closeout




# US 50/SR 132 Intersection Improvements Project

- Final punch list items
- Complete in early 2025
- Final Change Order on Agenda

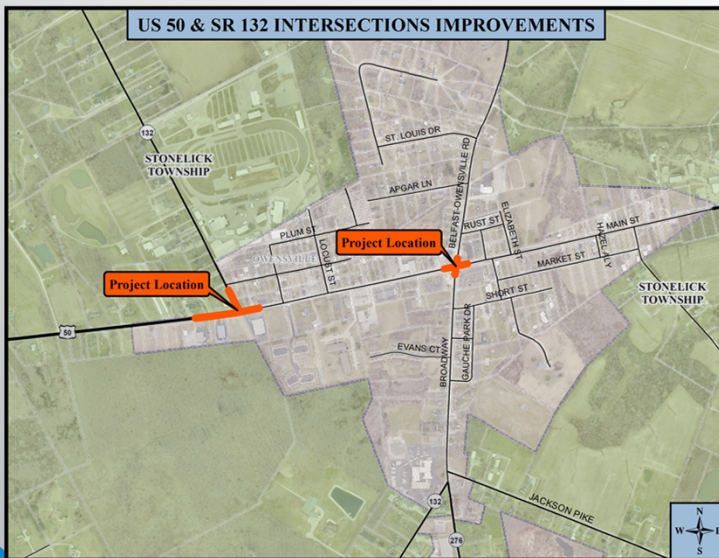



# Felicity Cedron Road Bridge Rehabilitation Project (C45-2.45)

- Stantec working on design
- FY26 Construction

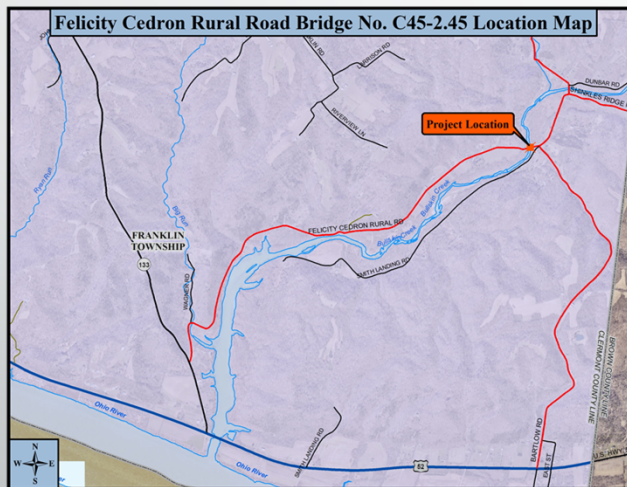


# District Drive – Rise Way Roadway Project

- Pending Miami Township determination of funding

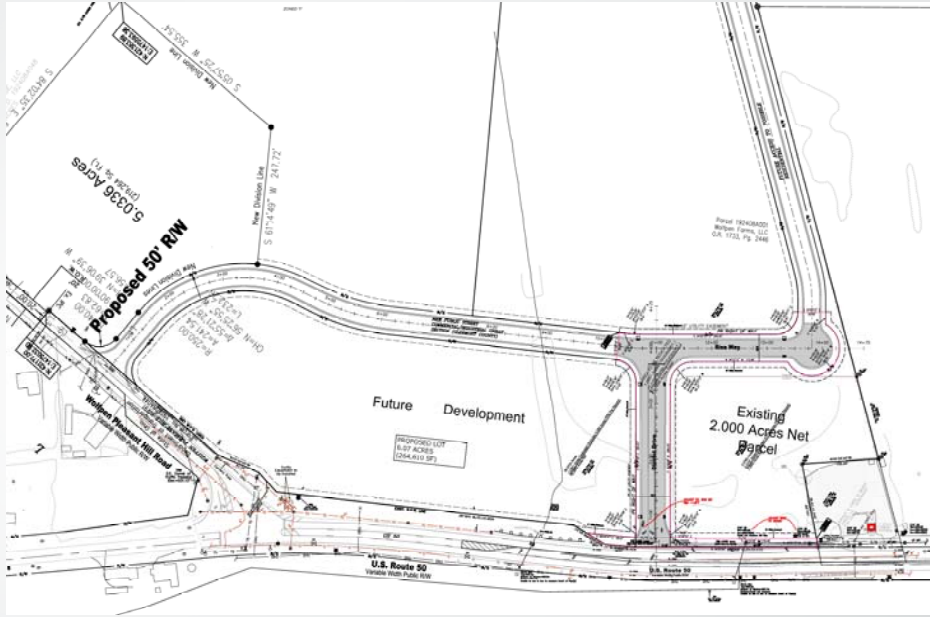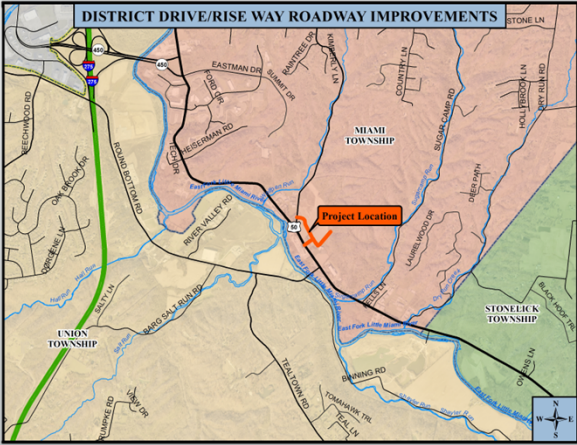


# Gibson Road Bridge Replacement (T194-1.30)

- Estimated start construction May
- Completion estimate - 8/1/2025

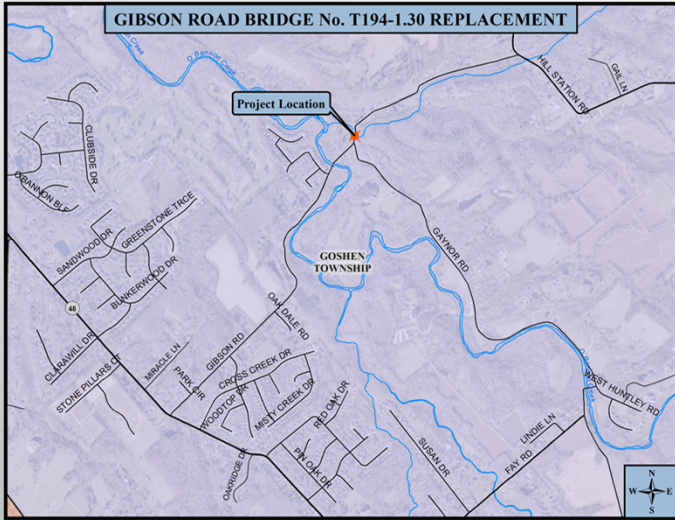


# Shiloh Road Bridge Replacement (C157-2.35)

- Shiloh road is scheduled to be closed on 2/17/25 and the project will start
- Completion Estimate – end of May

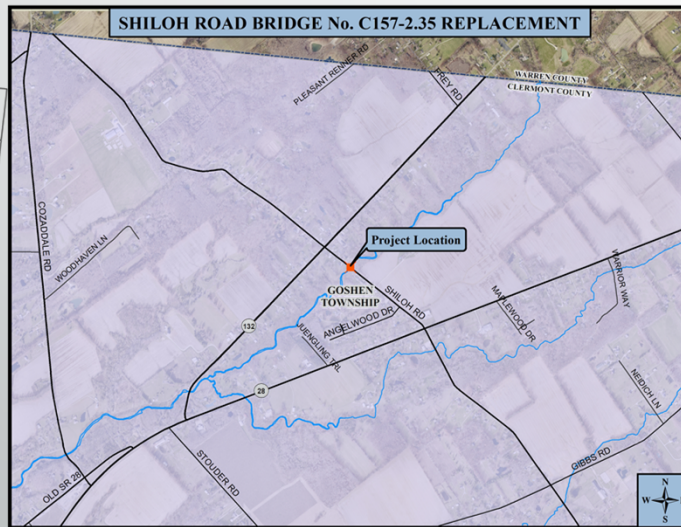


# Bray Road Bridge Replacement (T170—1.27)

- Construction in process
- Completion Estimate – end of April

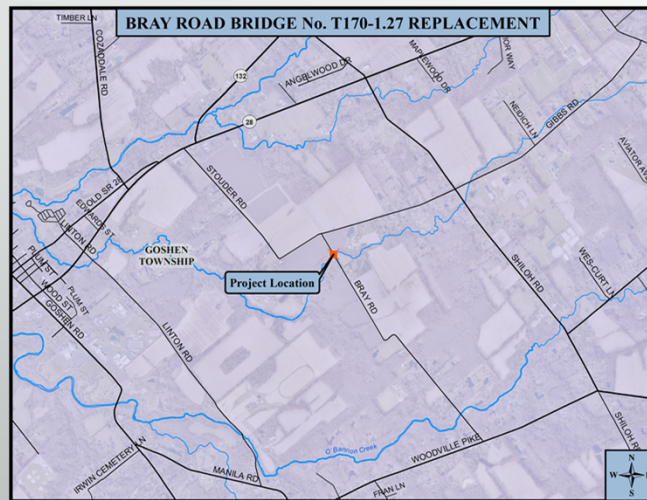


# Marathon Edenton Road Bridge Replacement (C82-1.61)

- Review of final drawings
- Prepare bids in May

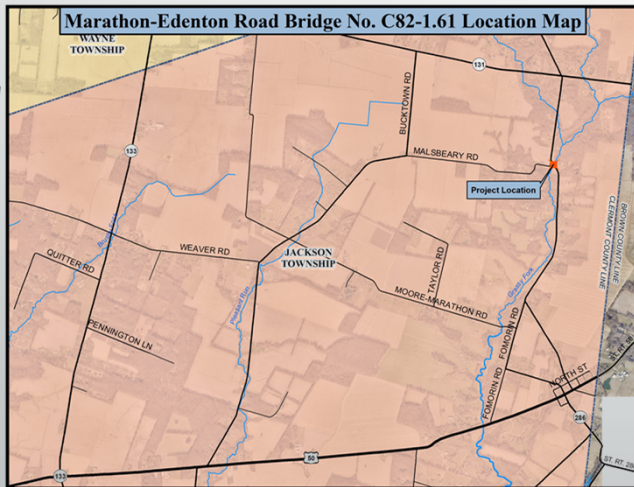



# Newtonsville Hutchinson Road Bridge Replacement (C93-2.08)

- Bidding to start in March

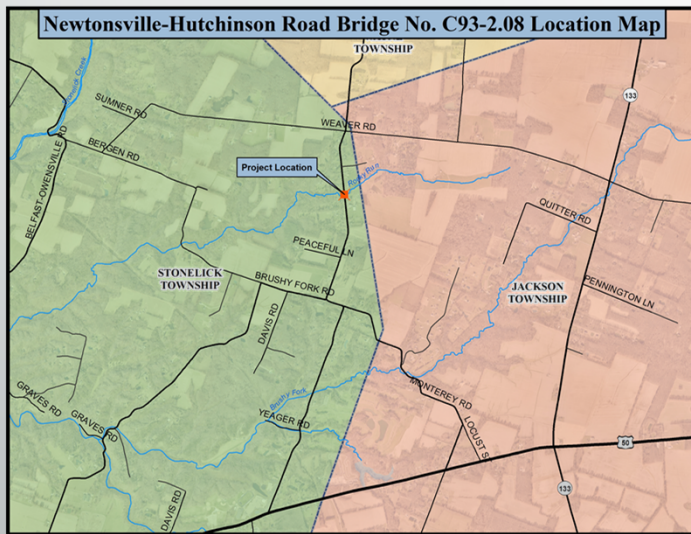

# Milford Schools Roadway Improvements

- Long Lead Materials on Order
- IGA Amendment and ROW Consultant Contract on TID Agenda

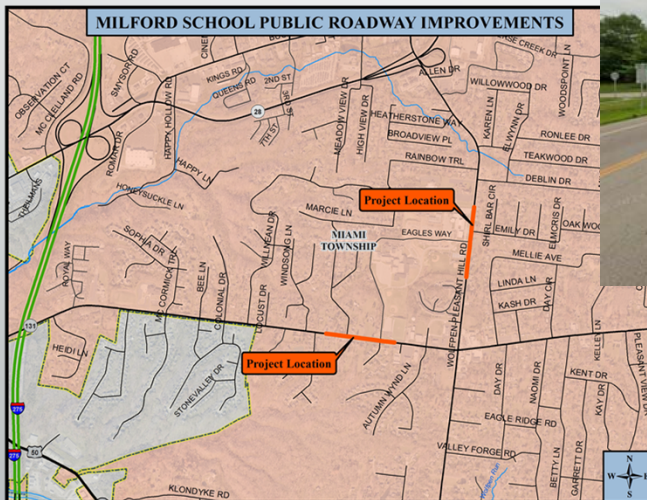

GEOMETRIC DATA - PLEASANT HILL ROAD			
STATION	DESCRIPTION	NOTHING	STARTING
48+72.00	PROPOSED WORK	8875.17	8880.00
48+48.00	END	8726.07	8740.00
28+48.00	END PROPOSED	7224.84	8800.00
28+47.26	END WORK	7224.84	8800.00

# Old SR 74/Elmont Drive

- Choice One contracted for design work
- Plans to be complete July 2025

