



Clermont County Transportation Improvement District

January 12, 2024


Pond Run Road Bridge Replacement (T767-2.86)

- Construction complete
- Road Opened 11-20-23
- Working through closeout



Round Bottom Road Bridge Replacement (C106-3.03)

- PS&E package submitted to ODOT
- Waiting on RR parcel
- Bidding in the next few months

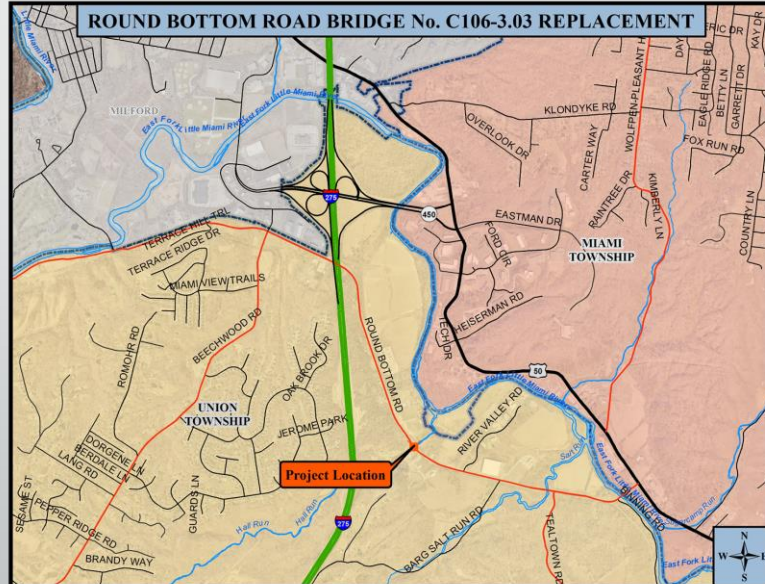


Aicholtz Road Roundabouts

- Utility relocation occurring now
- Contractor returning to site around March
- MOT TBD




Bach-Buxton Road Roundabouts

- CMAQ Request Unsuccessful
- Exploring Design Options and Path Forward

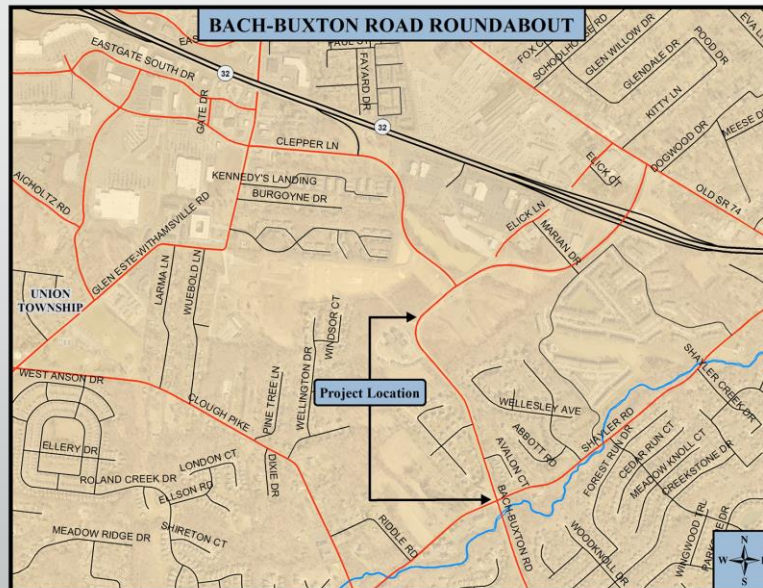


Deerfield Road and Woodville Pike Roundabouts

- Design Alternates Started
- Next Meeting in February
- 2028 Construction

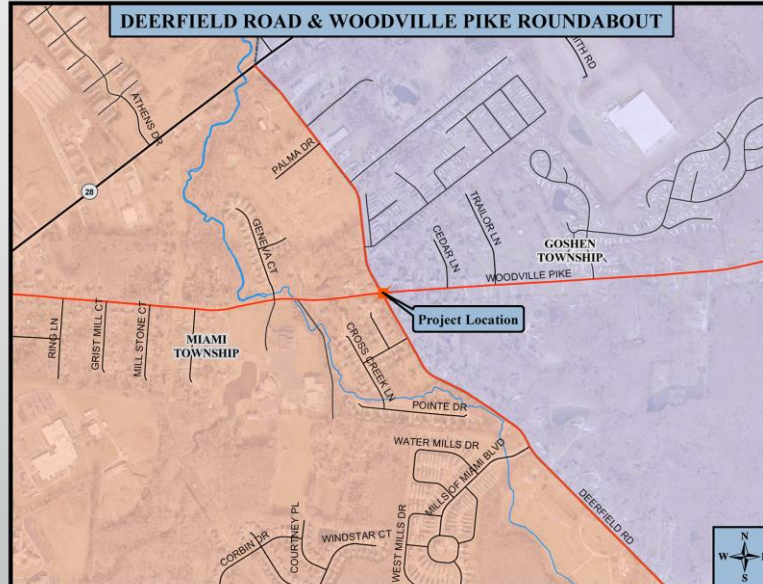


Ireton Trees Road Bridge Replacement (T39-1.20)

- Plans submitted to ODOT
- Bid in the next month when ODOT approves

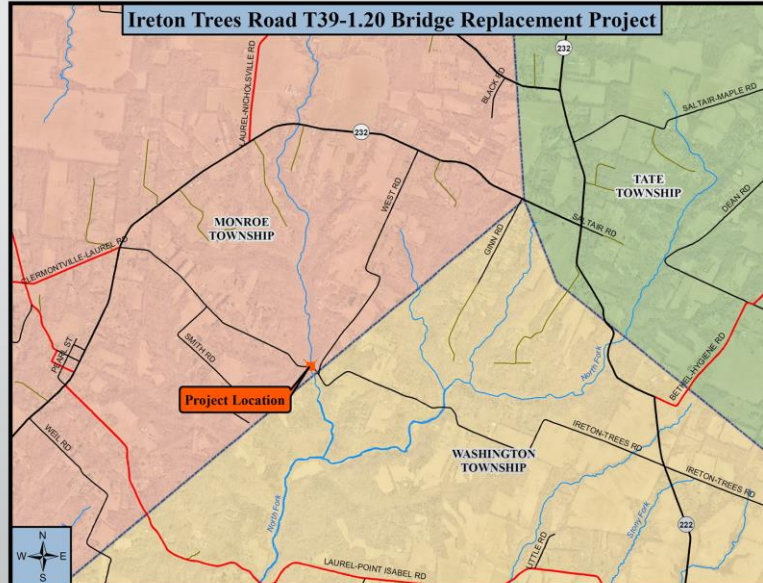


US 50/SR 132 Intersection Improvements Project

- Minor Plan Revisions
- Bid 1st Quarter 2024
- Complete by end of 2024

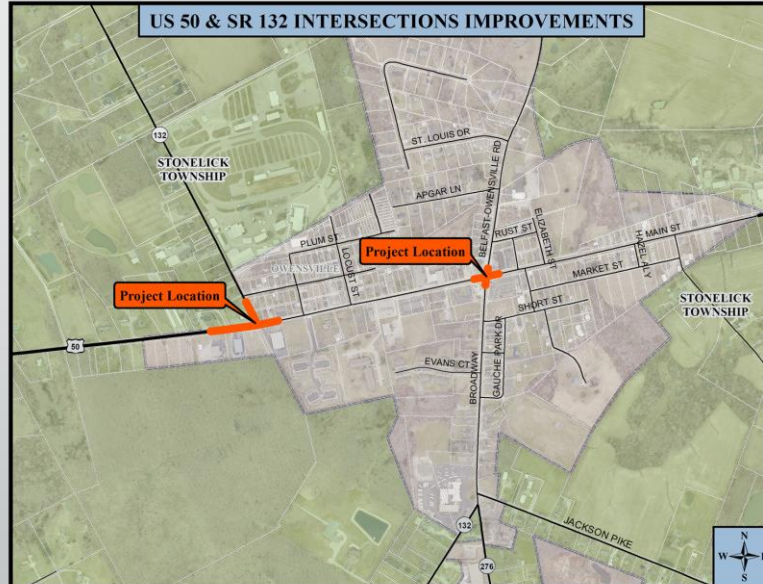

Felicity Cedron Road Bridge Rehabilitation Project (C45-2.45)

- 5 LOI Received
- Stantec Selected

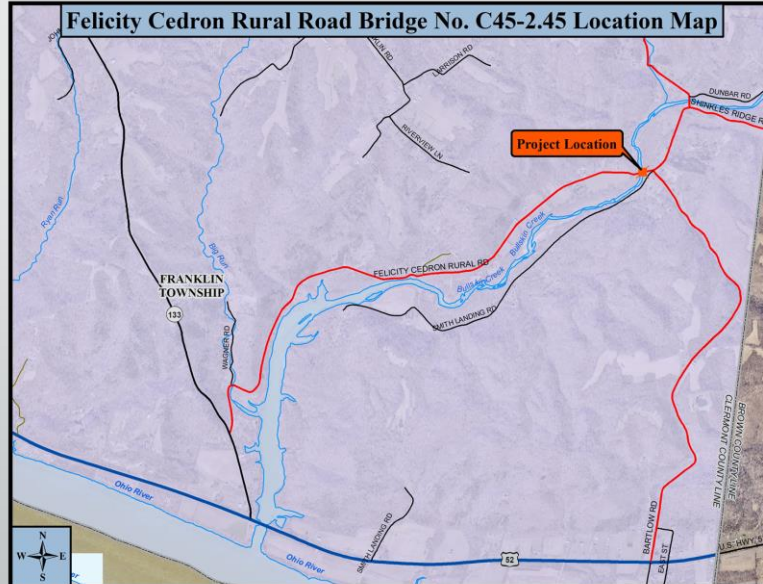

Champions Way Roadway Improvement

- Final Design Underway
- Bid 1st Quarter 2024

