




Clermont County Transportation Improvement District

June 14, 2024


Price Road Bridge Replacements (C76-0.28 & C76-0.40)

- Under Construction
- First bridge is complete
- Project complete by end of June

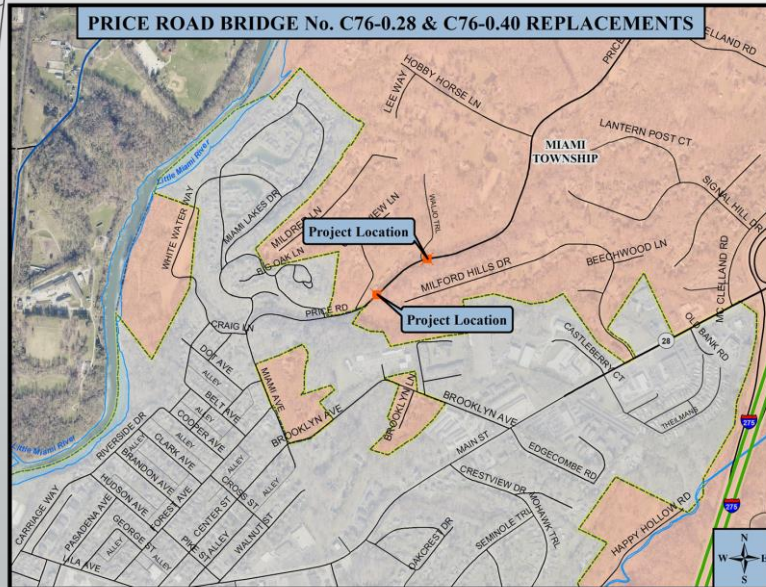


Round Bottom Road Bridge Replacement (C106-3.03)

- Bid Opening June 27

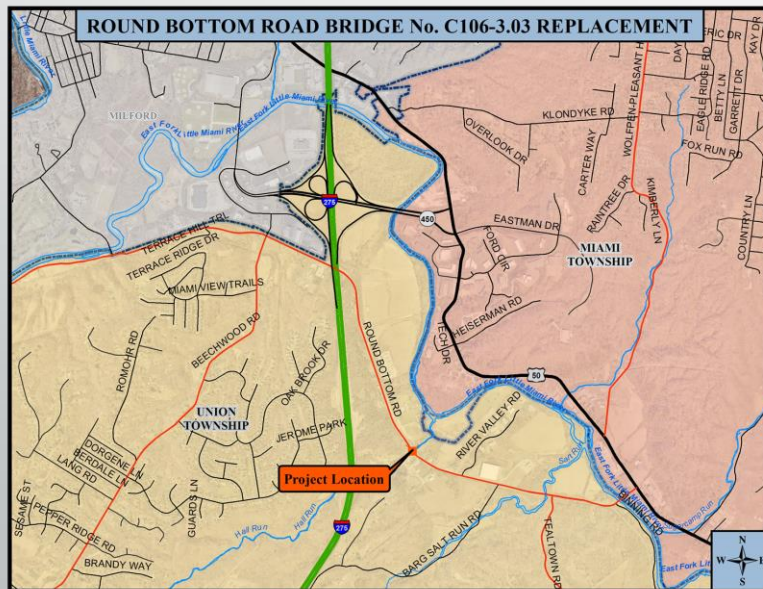


East Loveland Bridge Replacement (M01-0.18)

- Currently working on bridge
- Expect road to reopen by July

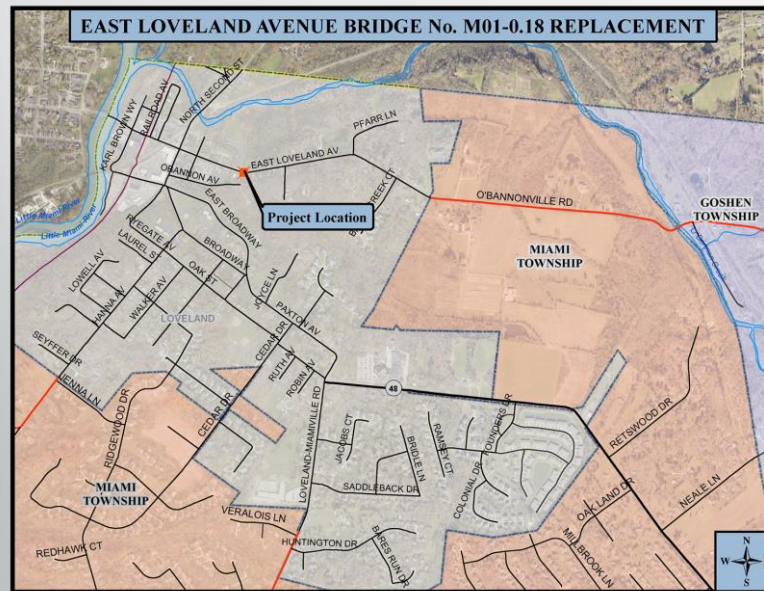


Aicholtz Road Roundabouts

- Utility relocation occurring now
- Glen Este is closed in the area and the contractor is working on storm installation.
- Various MOT situations over the coming months.
- Pouring curb and asphalt this week and next from RAB #1 to RAB #2

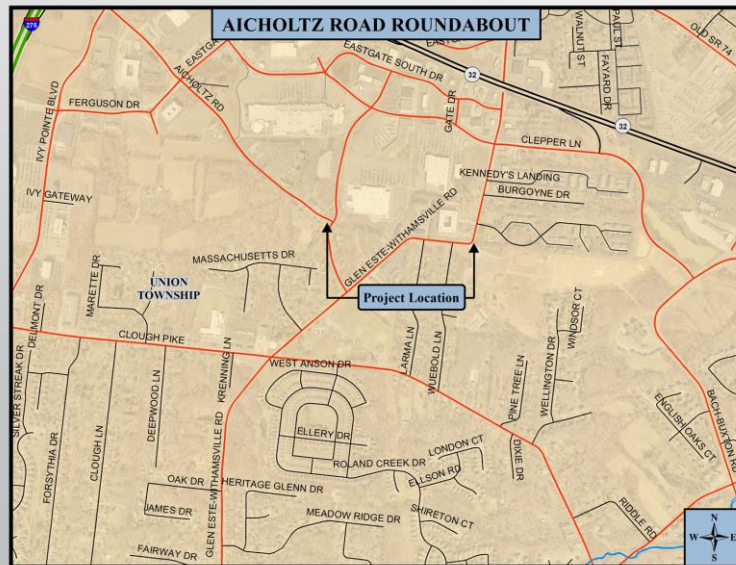


Bach-Buxton Road Roundabouts

- Coordination with Union Township on managing their sidewalk project
- Commissioners committed ARPA funds for Design assistance and Connect4Ohio funds for Construction
- OKI Grant Application submitted for construction phase

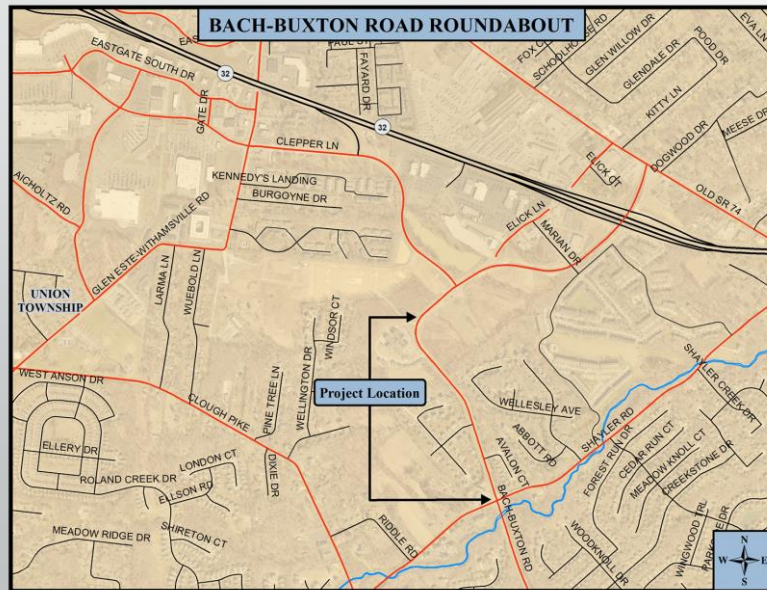


Deerfield Road and Woodville Pike Roundabouts

- Pre-Stage 1 Geometrics submitted for ODOT review
- 2028 Construction

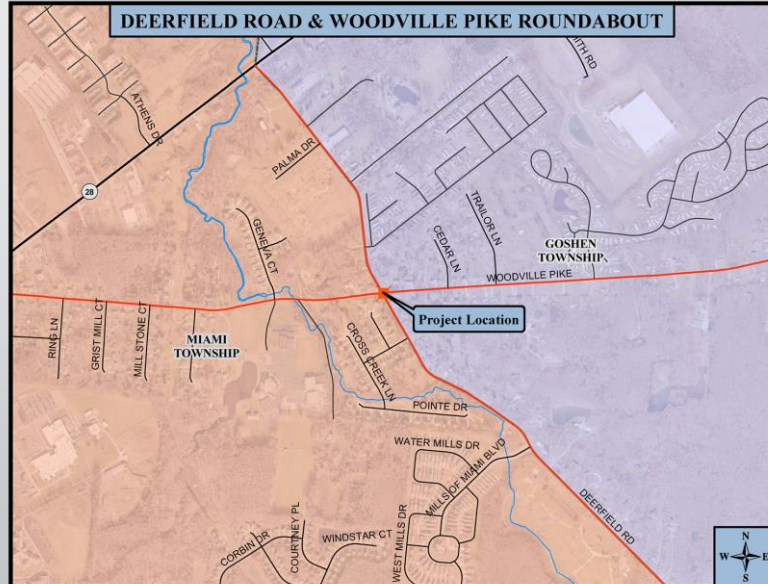


Glancy Corner- Marathon Road Bridge Rehabilitation (C54-2.16)

- Under contract for design

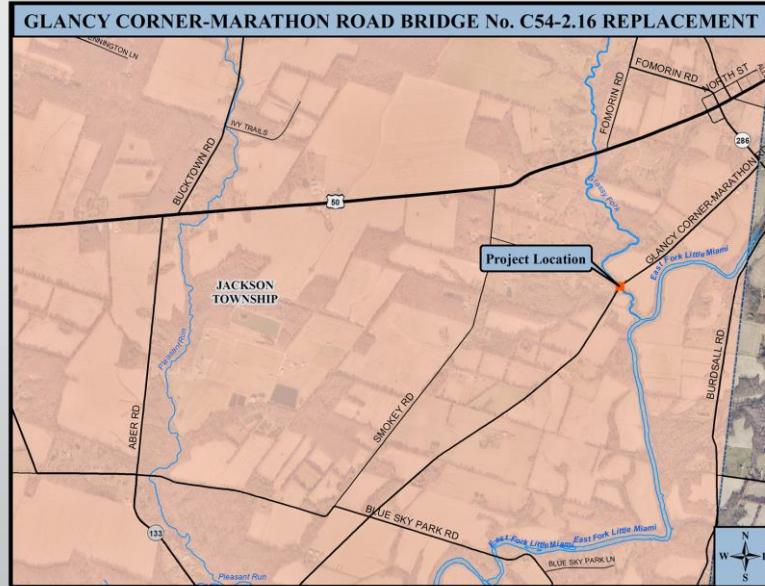


Ireton Trees Road Bridge Replacement (T39-1.20)

- Working towards construction contract.
- No schedule yet.

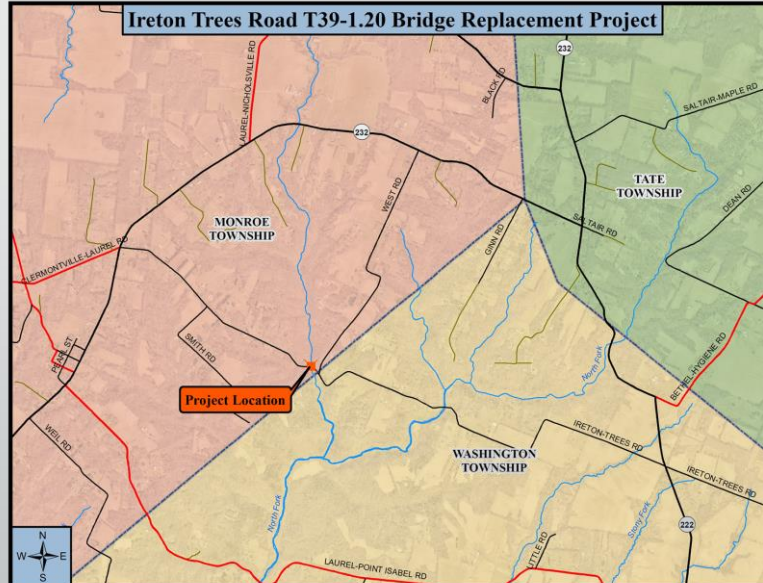


US 50/SR 132 Intersection Improvements Project

- Western Intersection
 - Widening along the north side of US 50 to be completed by the end of June
 - Widening along the south side of US 50 to be completed by July 19th
- Complete by end of 2024

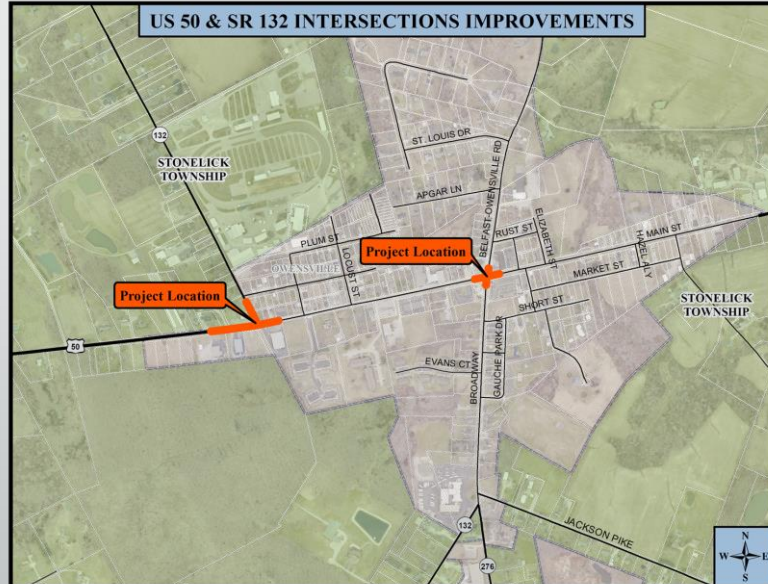



Felicity Cedron Road Bridge Rehabilitation Project (C45-2.45)

- Had our scoping meeting with Stantec and ODOT this week
- Expecting design proposal in the coming weeks.
- FY26 Construction

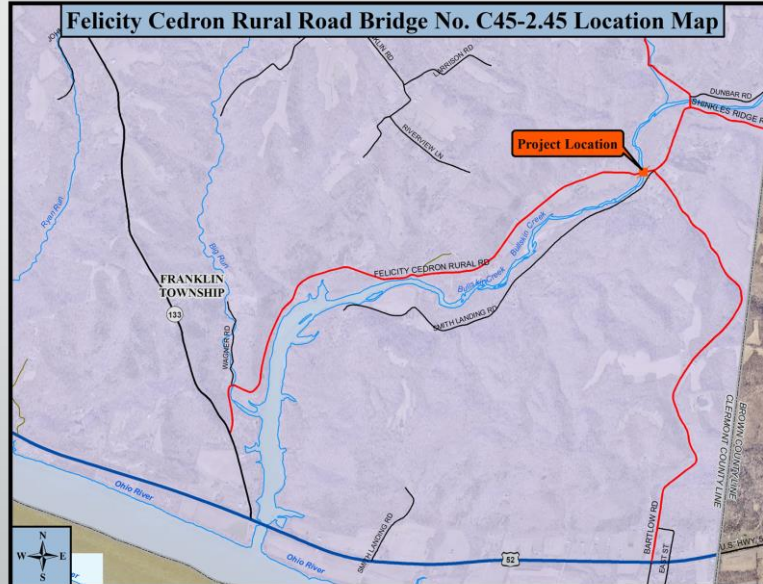

Champion's Way Roadway Improvement

- Contracted with KT Holden - \$1,018,686
- Pre-Construction meeting will be within the next couple weeks. No start date yet.

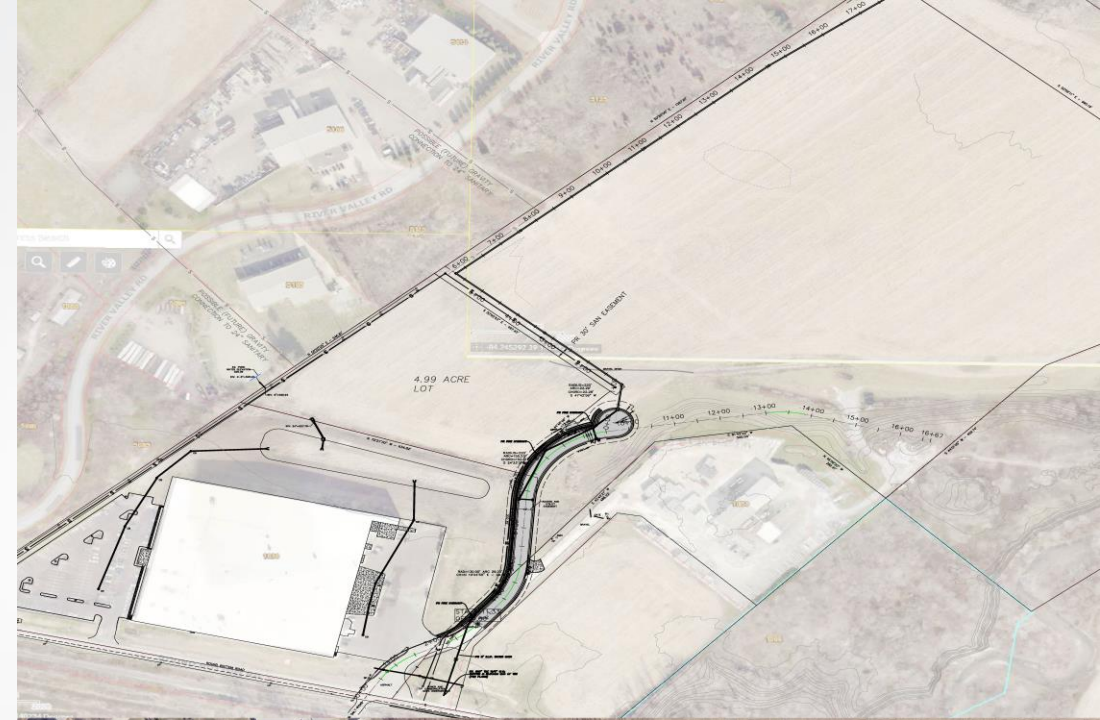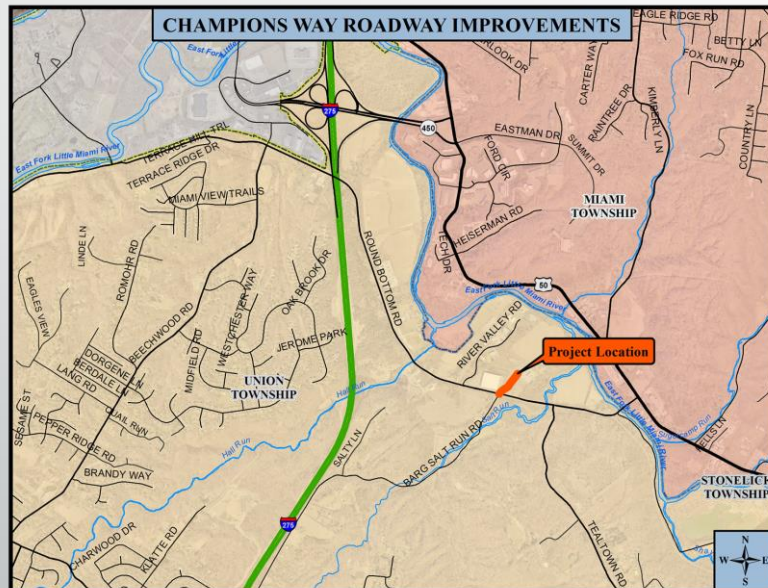

Neville-Penn Schoolhouse Landslide Repair

- Construction tentatively scheduled for August

