




# Clermont County Transportation Improvement District

August 9, 2024


# Round Bottom Road Bridge Replacement (C106-3.03)

- Under contract with JTM Smith Construction
- Contract completion by May 2, 2025

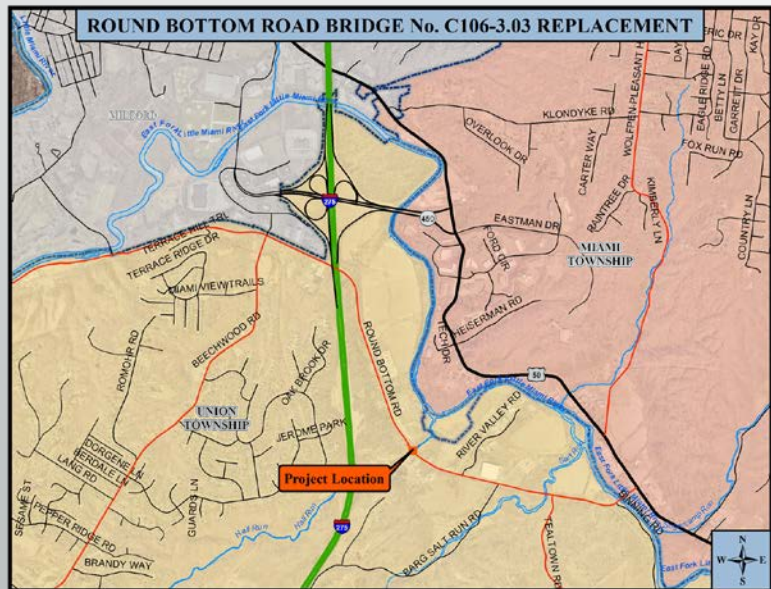


# East Loveland Bridge Replacement (M01-0.18)

- Majority of bridge work is complete, few minor railing issues to complete
- One lane is still supposed to happen within the next few weeks while crews continue to widen the road and install Sanitary lines.

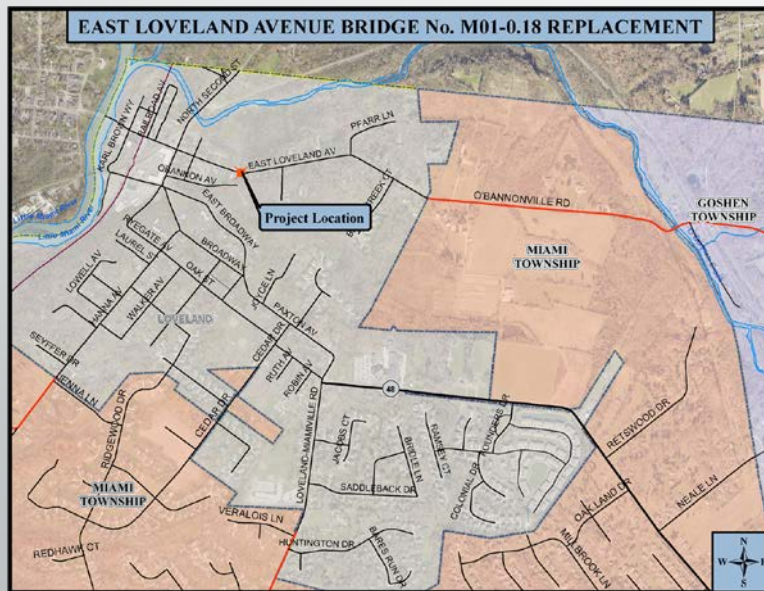


# Aicholtz Road Roundabouts

- Utility relocation is completed
- Work south of RAB #2 is almost completed
- Installing final asphalt course in the coming weeks from RAB #1 to RAB #3, then continue to final stretch of work from RAB #3 north

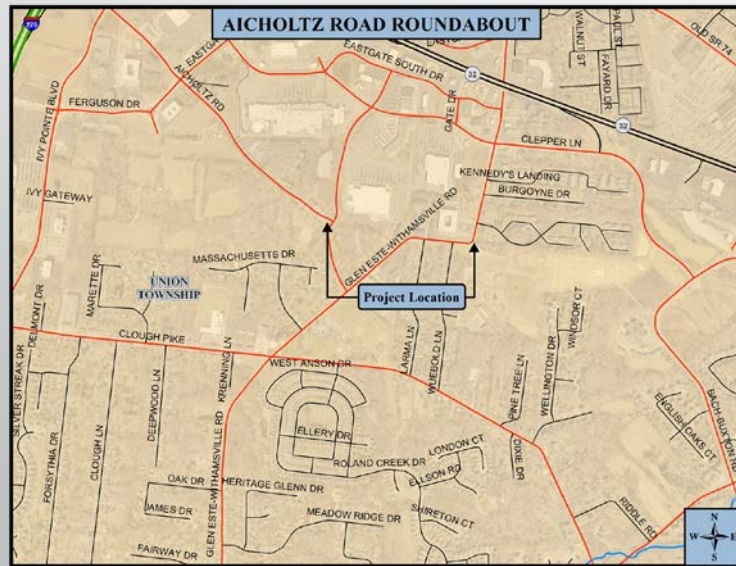


# Bach-Buxton Road Roundabouts

- Coordination with Union Township on managing their sidewalk project
- Agenda items for the Agreement and Change Order
- OKI Grant Application submitted for construction phase

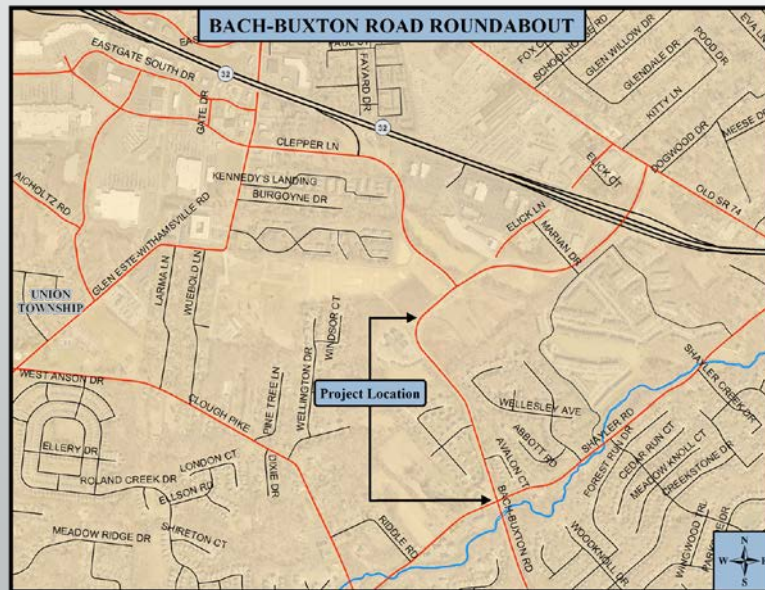


# Deerfield Road and Woodville Pike Roundabouts

- Preparing public involvement materials
- 2028 Construction

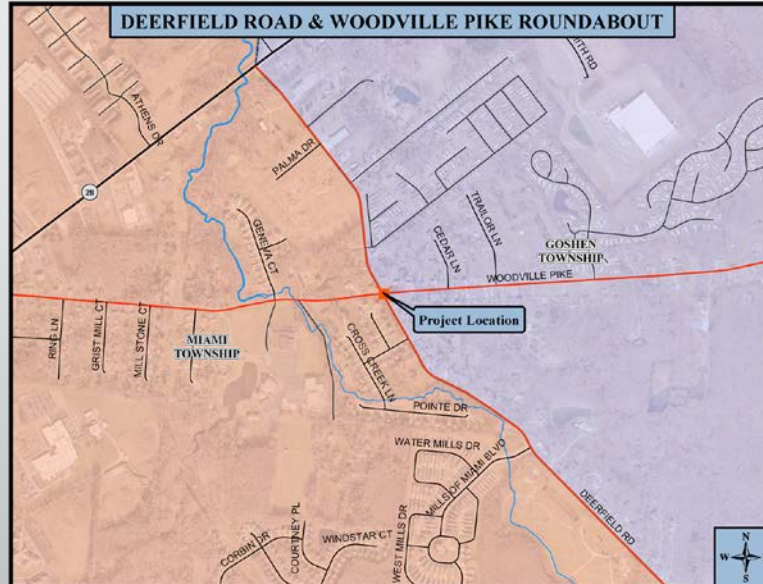


# Glancy Corner-Marathon Road Bridge Rehabilitation (C54-2.16)

- Under contract for design
- Stage 1 plans submitted to ODOT in June

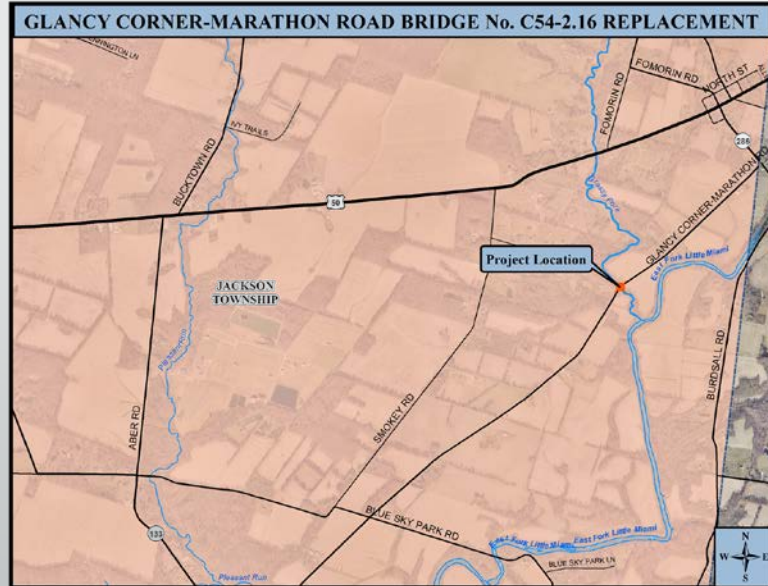

# Ireton Trees Road Bridge Replacement (T39-1.20)

- Under contract with KT Holden.
- Precon meeting within the next couple weeks to get a schedule

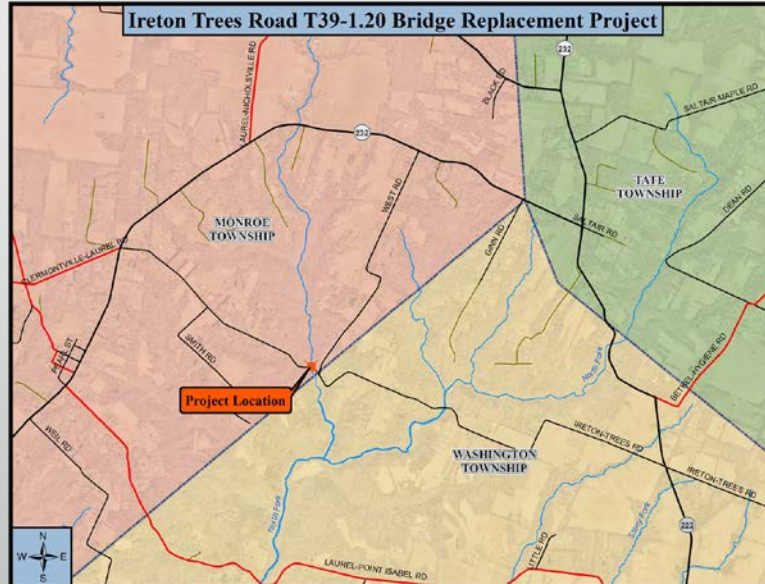


# US 50/SR 132 Intersection Improvements Project

- Western Intersection
  - Opened under temporary configuration
- Eastern Intersection
  - N. Broadway Closed on 7/29
- Complete by end of 2024




# Felicity Cedron Road Bridge Rehabilitation Project (C45-2.45)

- New business item to enter into agreement with Stantec Consulting
- FY26 Construction

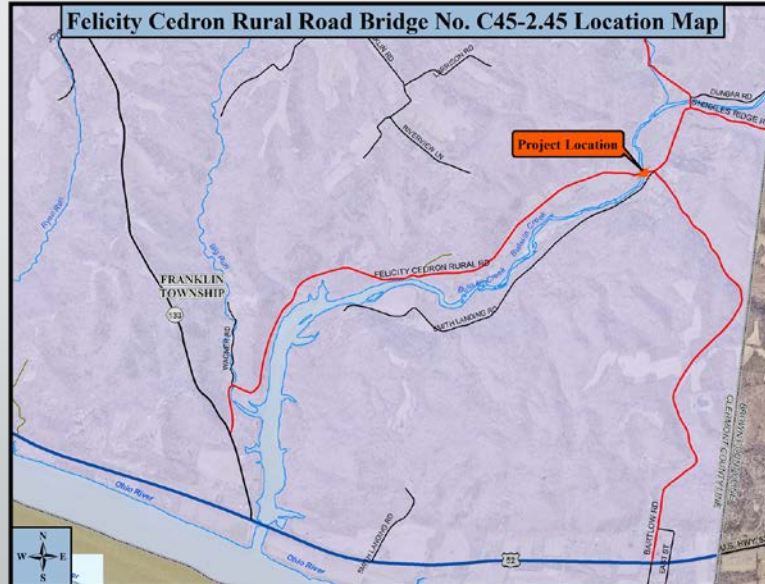

# Champion's Way Roadway Improvement

- Contracted with KT Holden - \$1,018,686
- Construction began this week. Stripping topsoil in preparation of storm work.

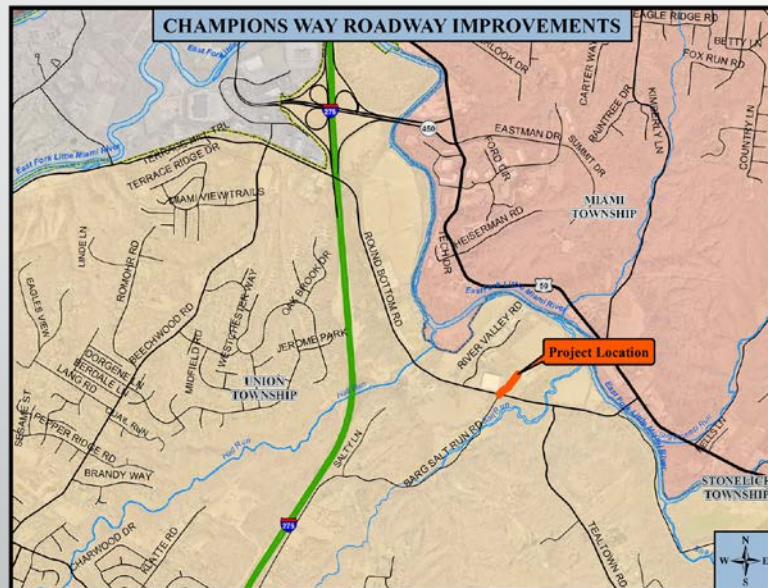

# Neville-Penn Schoolhouse Landslide Repair

- Construction tentatively scheduled for late August

