




Clermont County Transportation Improvement District

November 8, 2024


Round Bottom Road Bridge Replacement (C106-3.03)

- Construction may start this fall for utility relocation, waiting on pre-con for schedule
- Estimated completion – Early May, 2025

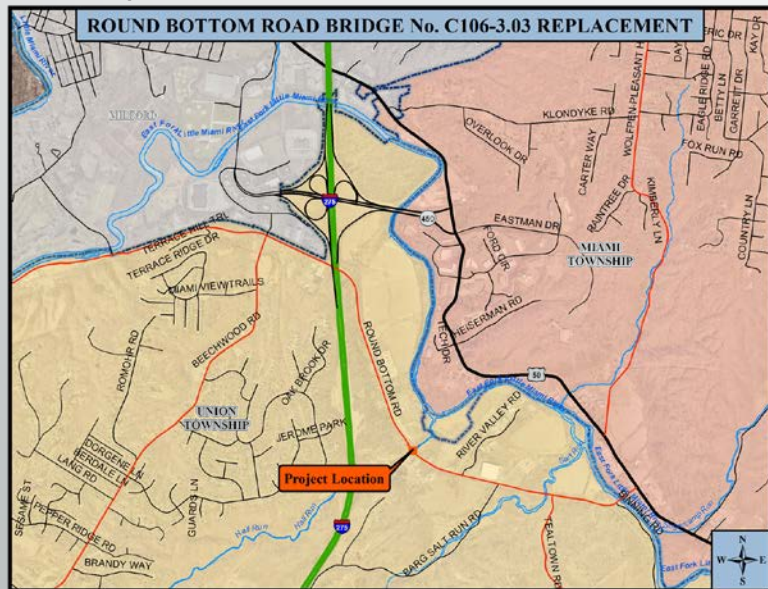


East Loveland Bridge Replacement (M01-0.18)

- Other than railing, the project is complete and open

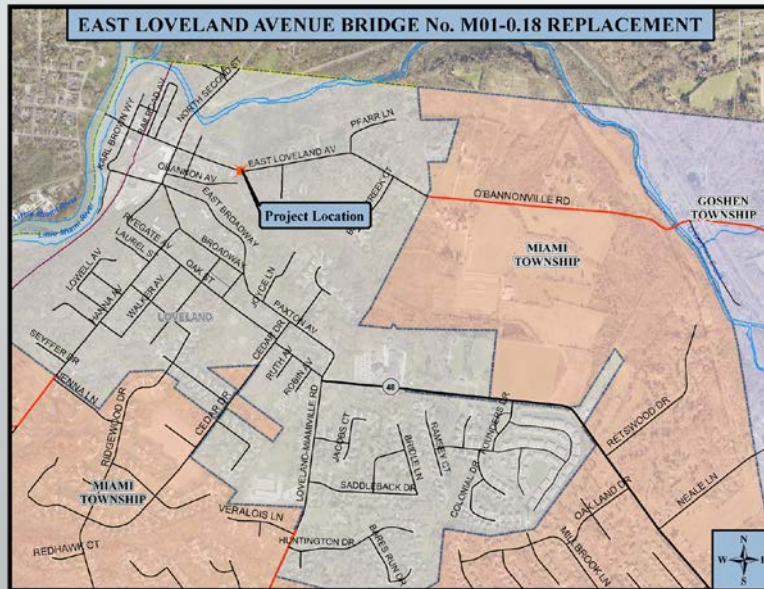


Aicholtz Road Roundabouts

- Project is now fully open to the public.
- Waiting on Duke for power to lighting.
- Finishing up signage, and minor punch list items

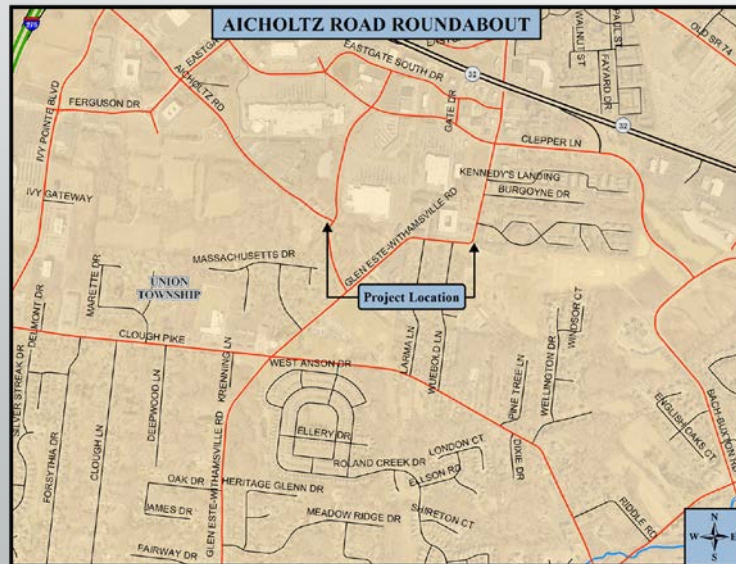


Bach-Buxton Road Roundabouts

- OKI approved \$2.8M of \$3.3M STBG funds requested

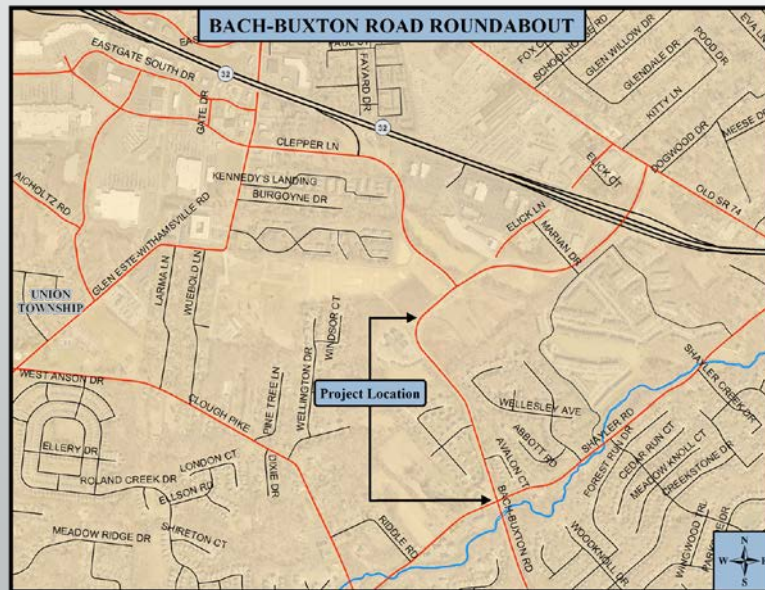


Deerfield Road and Woodville Pike Roundabouts

- Public comment period closed October 20th
- 2028 Construction

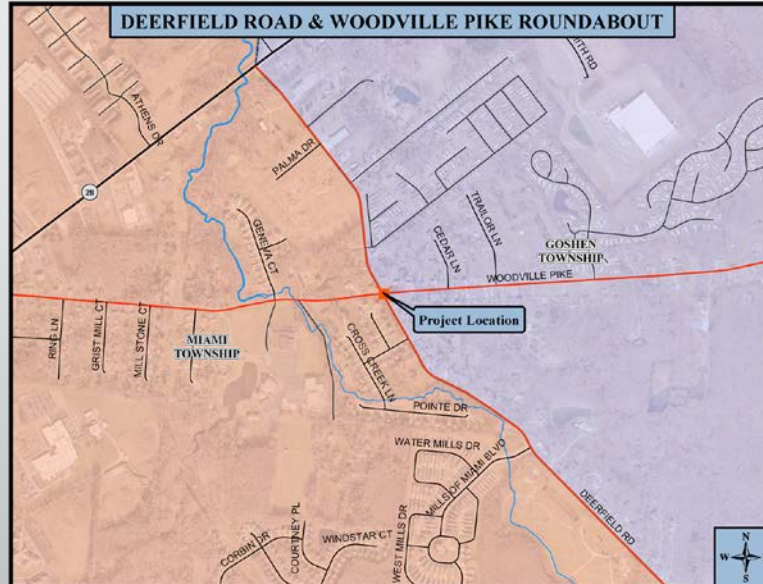


Glancy Corner-Marathon Road Bridge Rehabilitation (C54-2.16)

- Received ODOT review in early October
- B&N has addressed ODOT review and has submitted stage 3 plans for review.

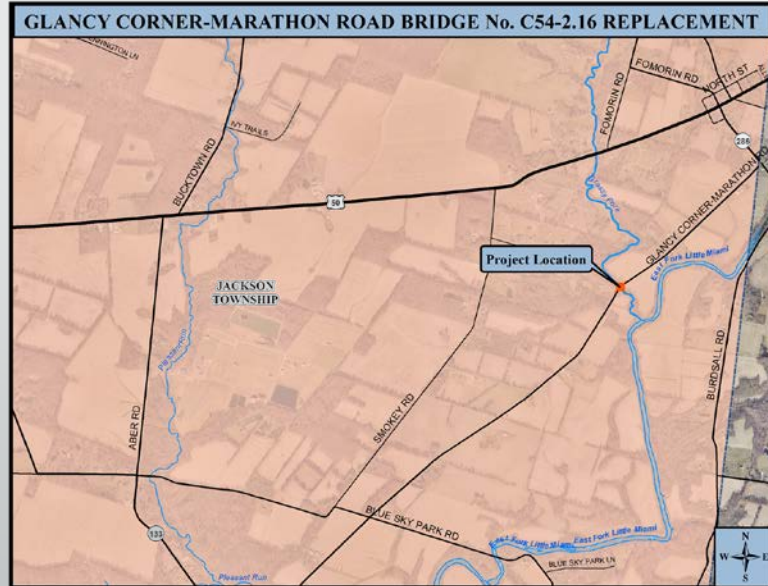


Ireton Trees Road Bridge Replacement (T39-1.20)

- Project is completed with a few minor issues remaining (waiting on Guardrail material)

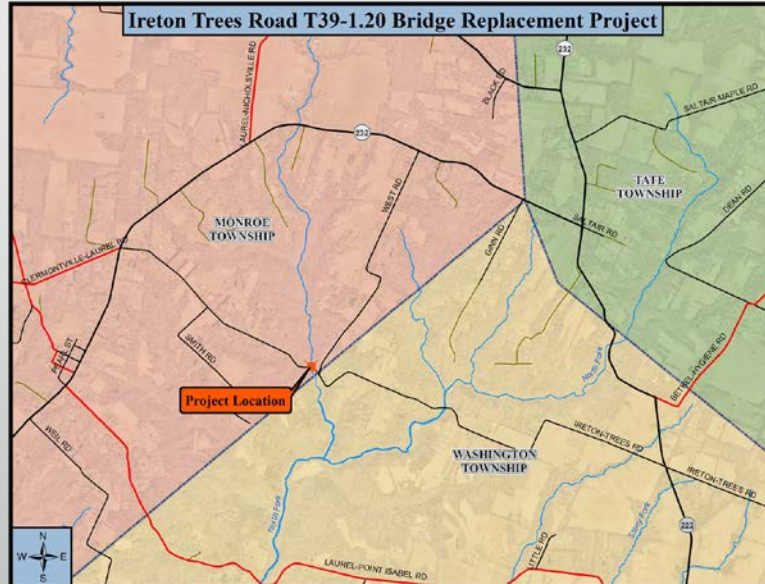


US 50/SR 132 Intersection Improvements Project

- Work to be completed:
 - Final surface and striping
 - Signal Installation
- Complete by end of 2024

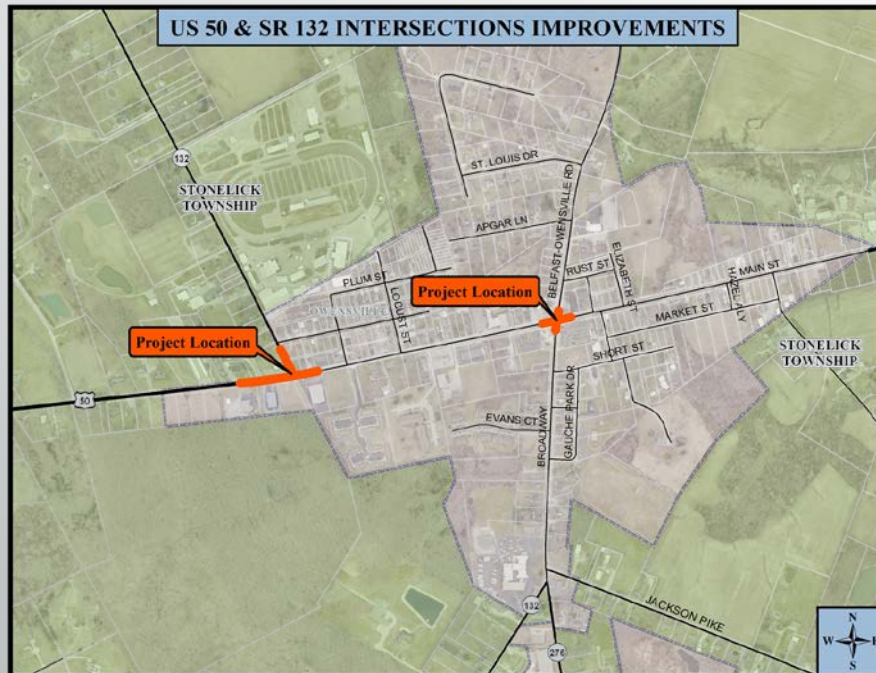


Felicity Cedron Road Bridge Rehabilitation Project (C45-2.45)

- Stantec working on design
- FY26 Construction

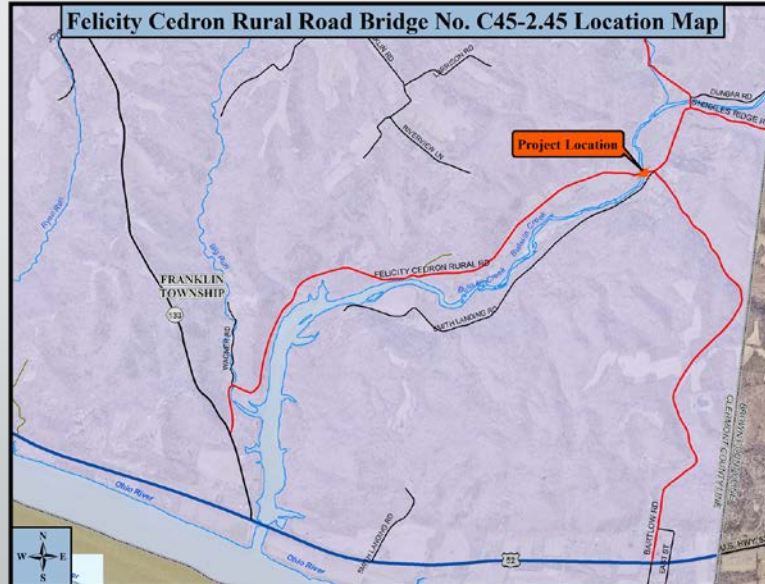

Champion's Way Roadway Improvement

- Project is complete, working on final payments and closeout.

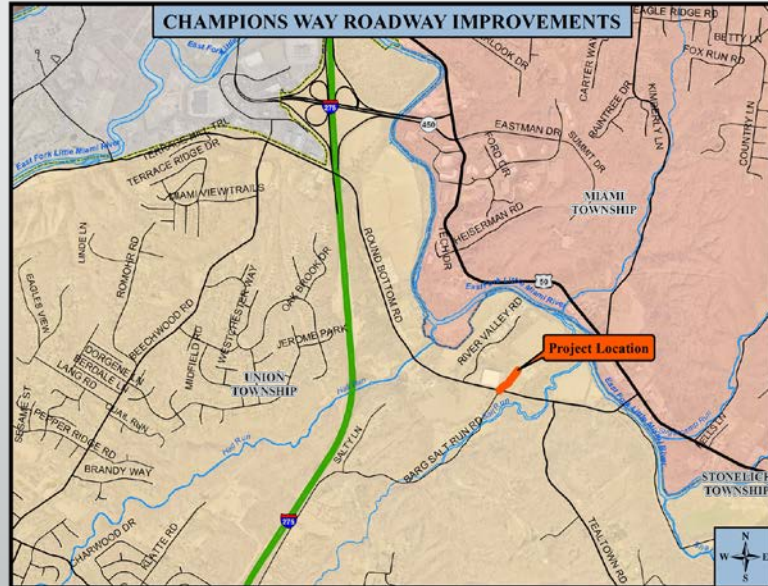



Neville-Penn Schoolhouse Landslide Repair

- Construction Completed
September 23rd



District Drive – Rise Way Roadway Project

- Pending Miami Township determination of funding

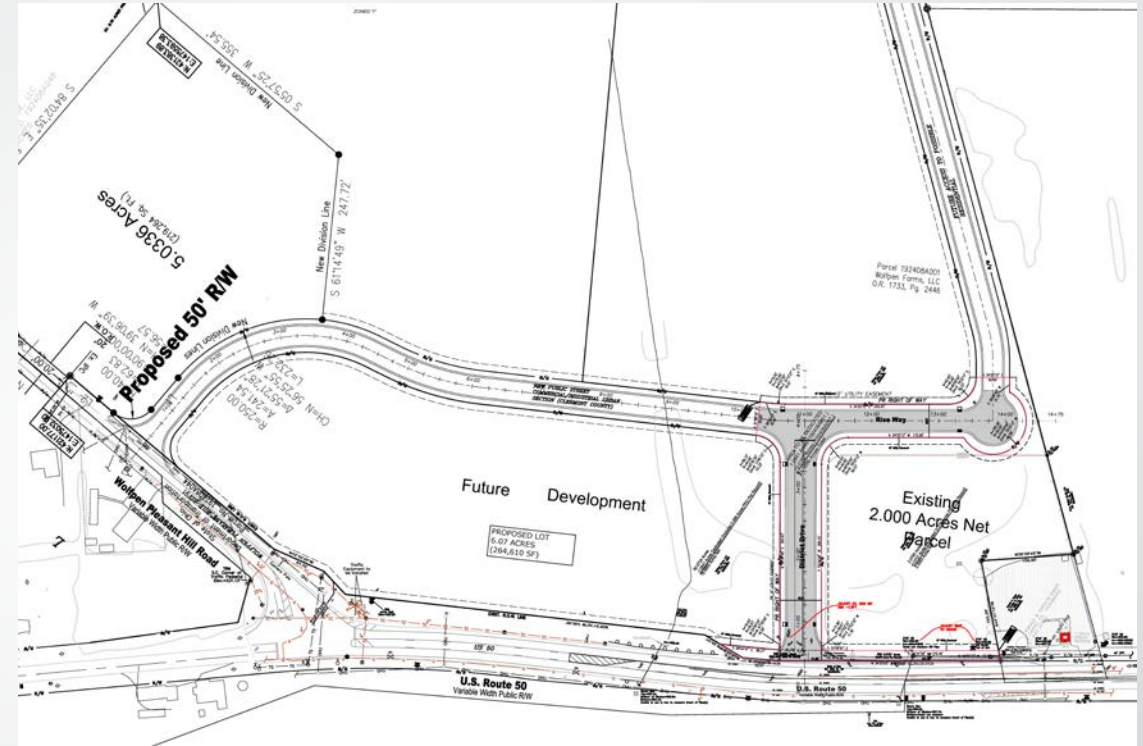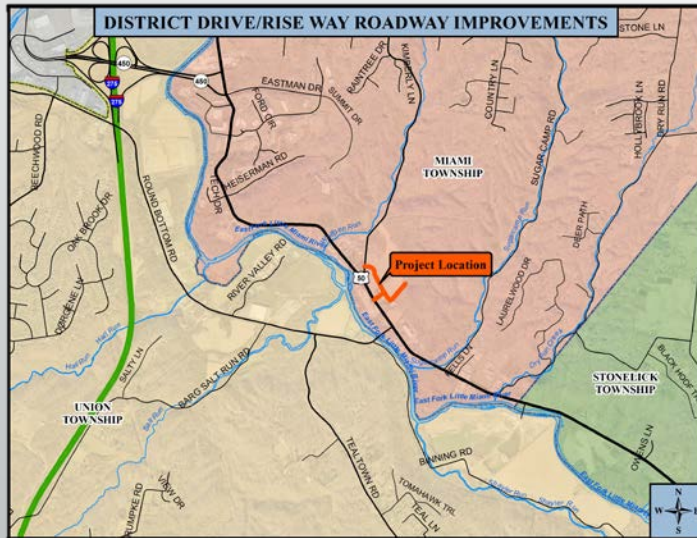

Gibson Road Bridge Replacement (T194-1.30)

- Bids opened October 17, 2024
- JTM Construction was the apparent low bidder at \$590,156.
- Working on contracts and schedule
- Complete by 8/1/2025



Shiloh Road Bridge Replacement (C157-2.35)

- Bids opened October 3, 2024
- Apparent Low bidder – JTM Smith
- \$278,458.67
- Working on contracts and schedule
- Complete by 8/1/2025




Bray Road Bridge Replacement (T170—1.27)

- Bids opened October 10, 2024
- Apparent Low bidder – JTM Smith
- \$269,866.75
- Working on contracts and schedule
- Complete by 8/1/2025



Marathon Edenton Road Bridge Replacement (C82-1.61)

- Working on final drawings.
- Bid when drawings are complete and final ROW is acquired.

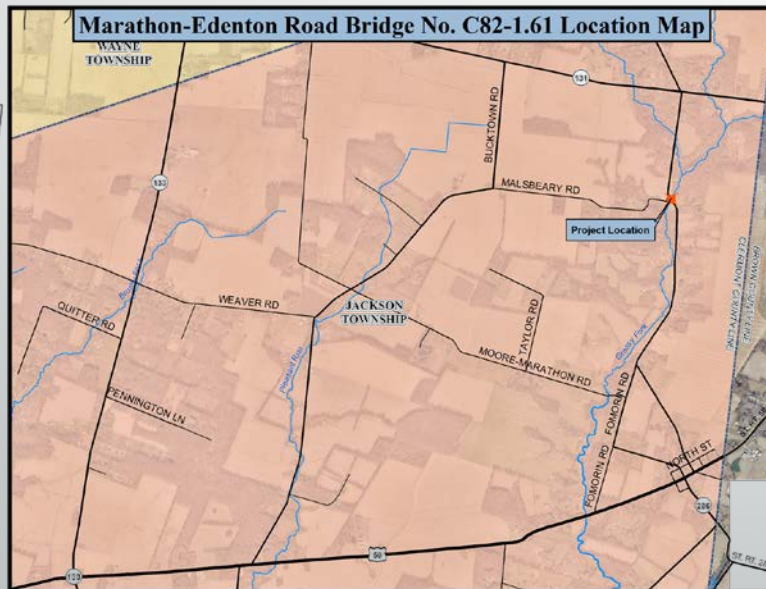

Newtonsville Hutchinson Road Bridge Replacement (C93-2.08)

- Working on final ROW
- Bid project after ROW by end of 2024

