




# Clermont County Transportation Improvement District

February 9, 2024


# Price Road Bridge Replacements (C76-0.28 & C76-0.40)

- Under Construction
- Awarding contract to DDK
- Project complete by June 15<sup>th</sup>

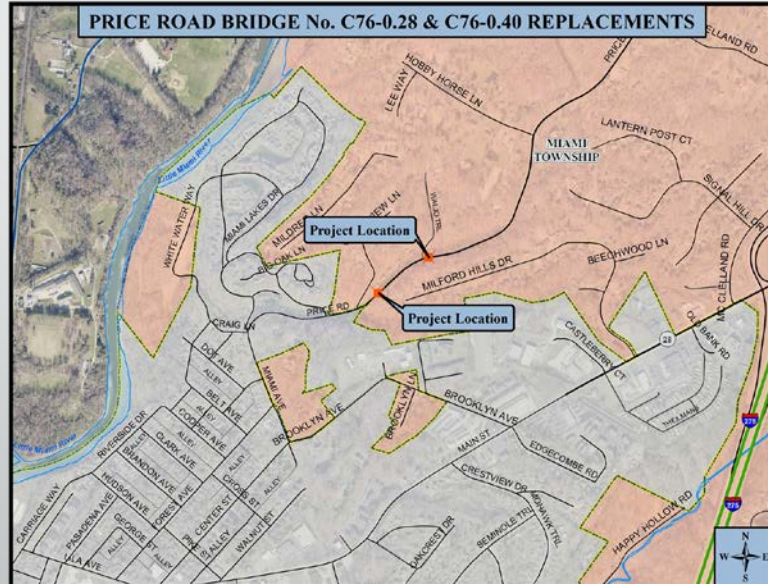

# Round Bottom Road Bridge Replacement (C106-3.03)


- PS&E package submitted to ODOT
- ROW Certified
- Bidding in the next few months

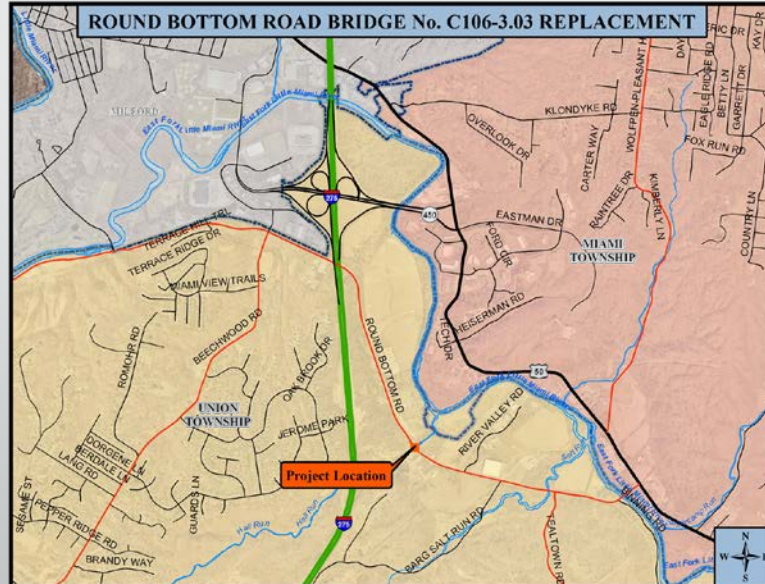




# Aicholtz Road Roundabouts

- Utility relocation occurring now
- Contractor returning to site around March
- MOT meetings last month

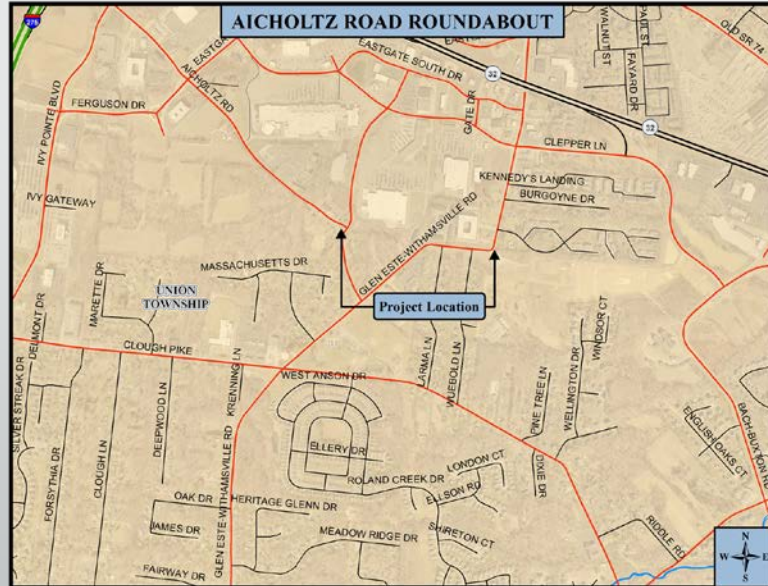


# Bach-Buxton Road Roundabouts

- Exploring Design Options and Path Forward

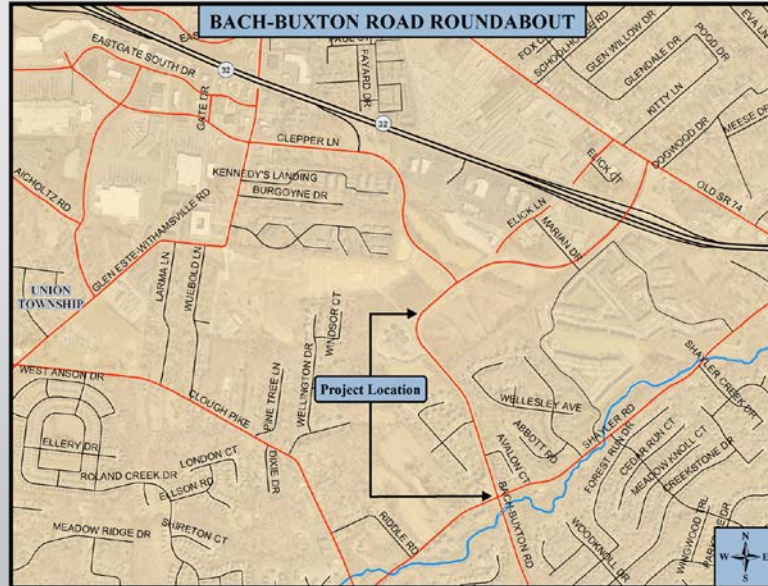


# Deerfield Road and Woodville Pike Roundabouts

- Met to Review Design Alternates and Discuss Schedule
- 2028 Construction

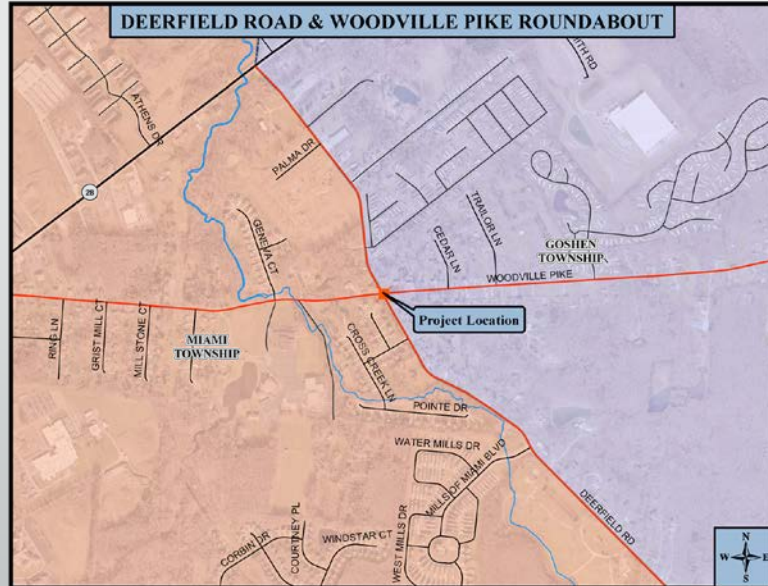


# Glancy Corner-Marathon Road Bridge Rehabilitation (C54-2.16)

- ODOT scoping meeting complete
- ODOT agreement coming soon
- Preparing design contracts with B&N which is 100% CEAO funded

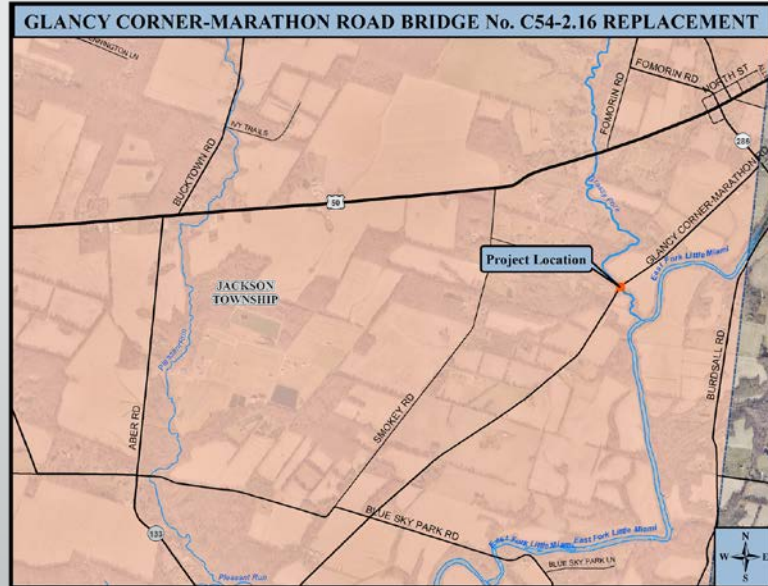


# Ireton Trees Road Bridge Replacement (T39-1.20)

- Plans submitted to ODOT
- Bid in the next month when ODOT approves PSE Submittal

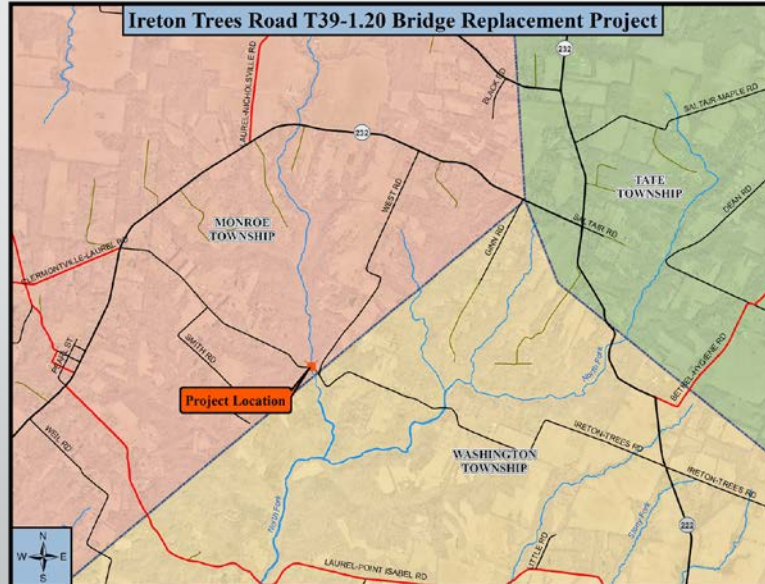


# US 50/SR 132 Intersection Improvements Project

- Bid published Feb 8
- Bid opening Feb 29
- Complete by end of 2024

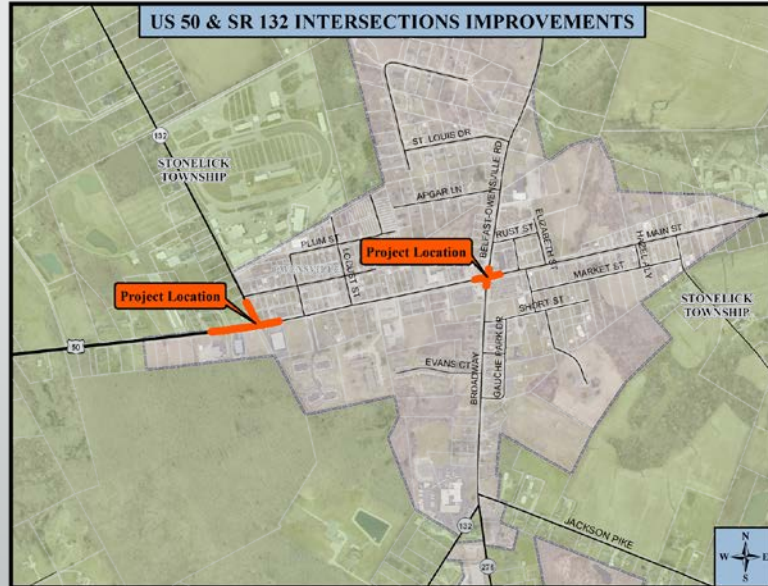

# Felicity Cedron Road Bridge Rehabilitation Project (C45-2.45)

- Scoping meeting and fee proposal in process with Stantec and ODOT

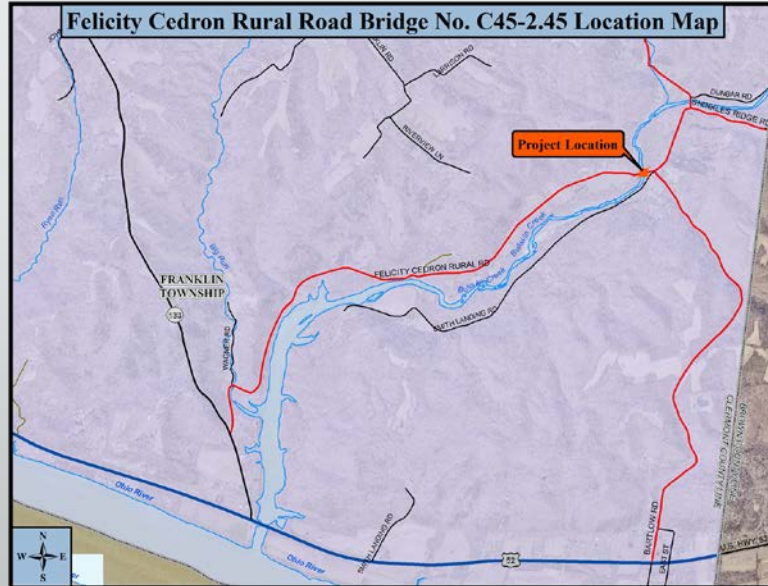

# Champion's Way Roadway Improvement

- Final Design Underway
- Bid 1<sup>st</sup> Quarter 2024

