




Clermont County Transportation Improvement District

April 11, 2025


Round Bottom Road Bridge Replacement (C106-3.03)

- Watermain is completed
- Abutments have been installed and the beams are now set.
- Completion Estimate— May 2025

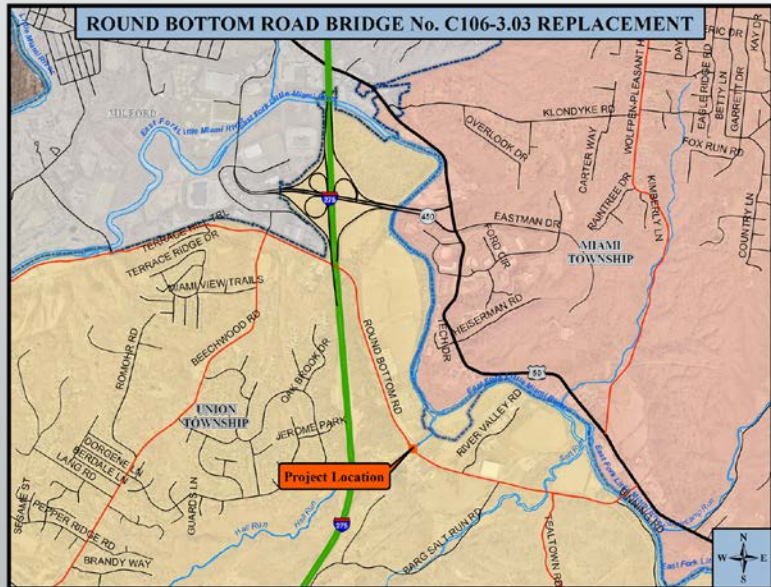


Bach-Buxton Road Roundabouts

- ODOT scoping completed
- Schedule being revised
- Feasibility submittal due this spring

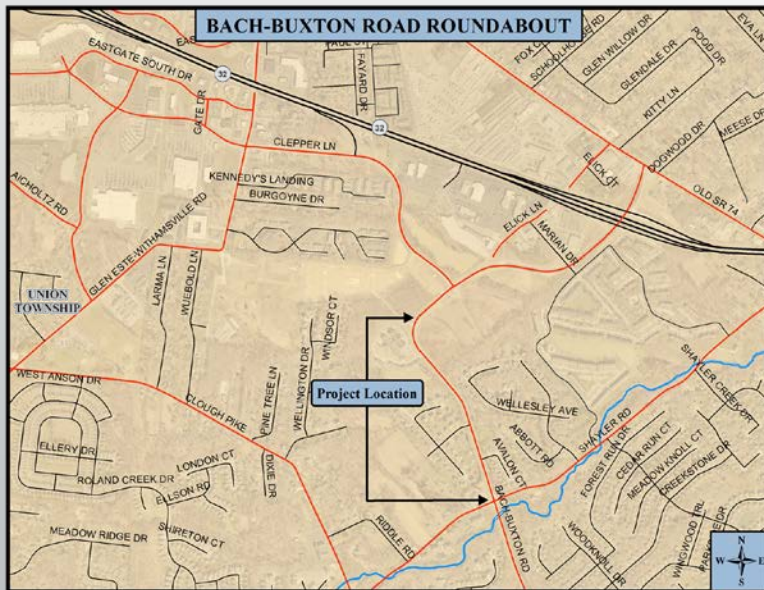


Deerfield Road and Woodville Pike Roundabouts

- Addressing Stage 1 comments and preparing for Stage 2 submittal
- 2028 Construction

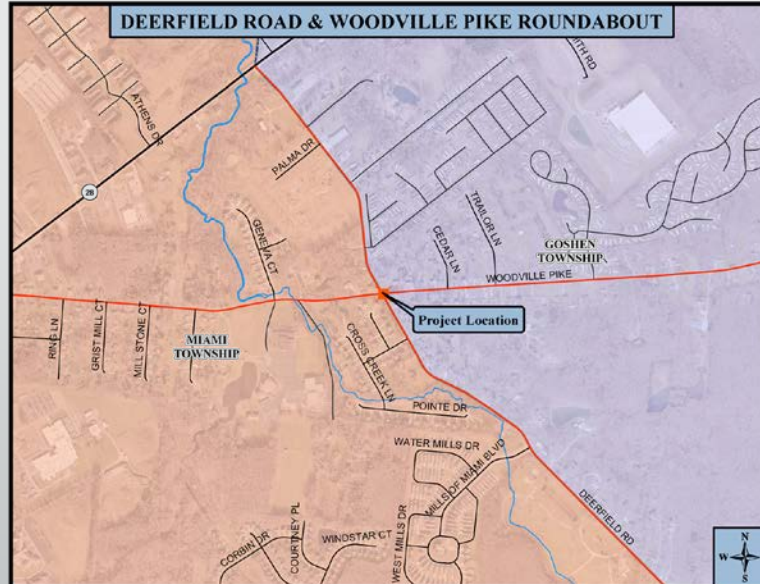

Glancy Corner-Marathon Road Bridge Rehabilitation (C54-2.16)

- Project is currently out for public bid
- Bids will be opened on April 24th

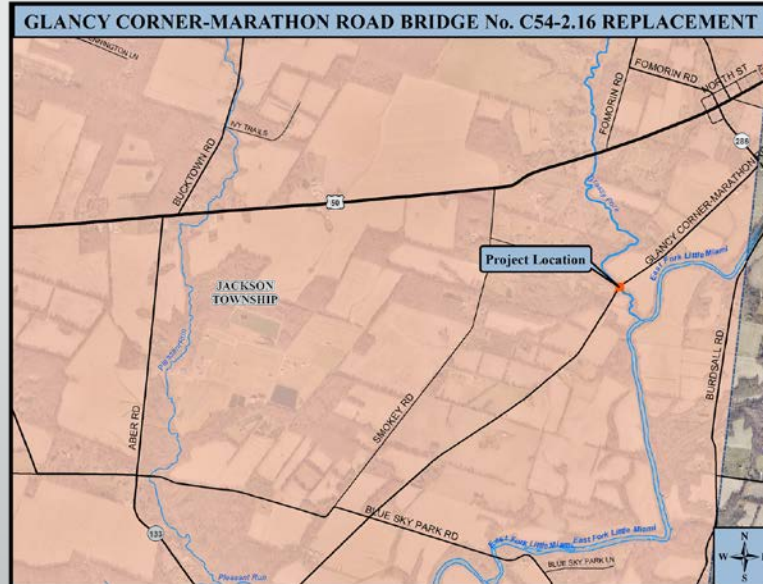



Felicity Cedron Road Bridge Rehabilitation Project (C45-2.45)

- Finalizing stage 1 review along with ODOT's review
- FY26 Construction




District Drive – Rise Way Roadway Project

- Funding established
- Project will bid after final approval of plans
- Contract award authorization on agenda

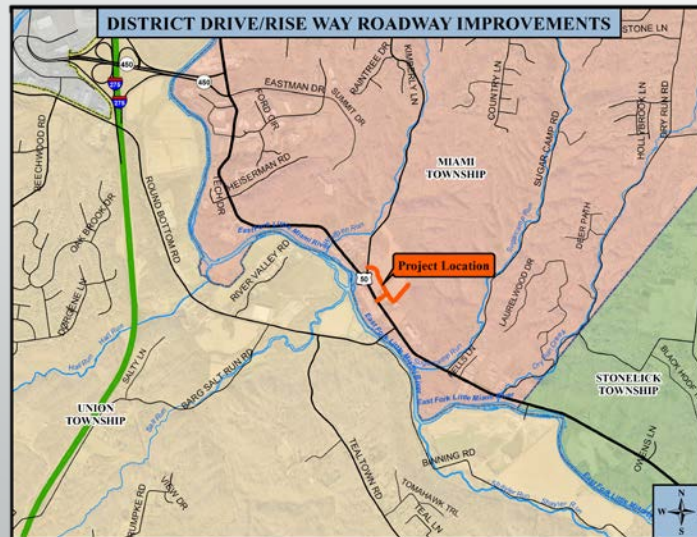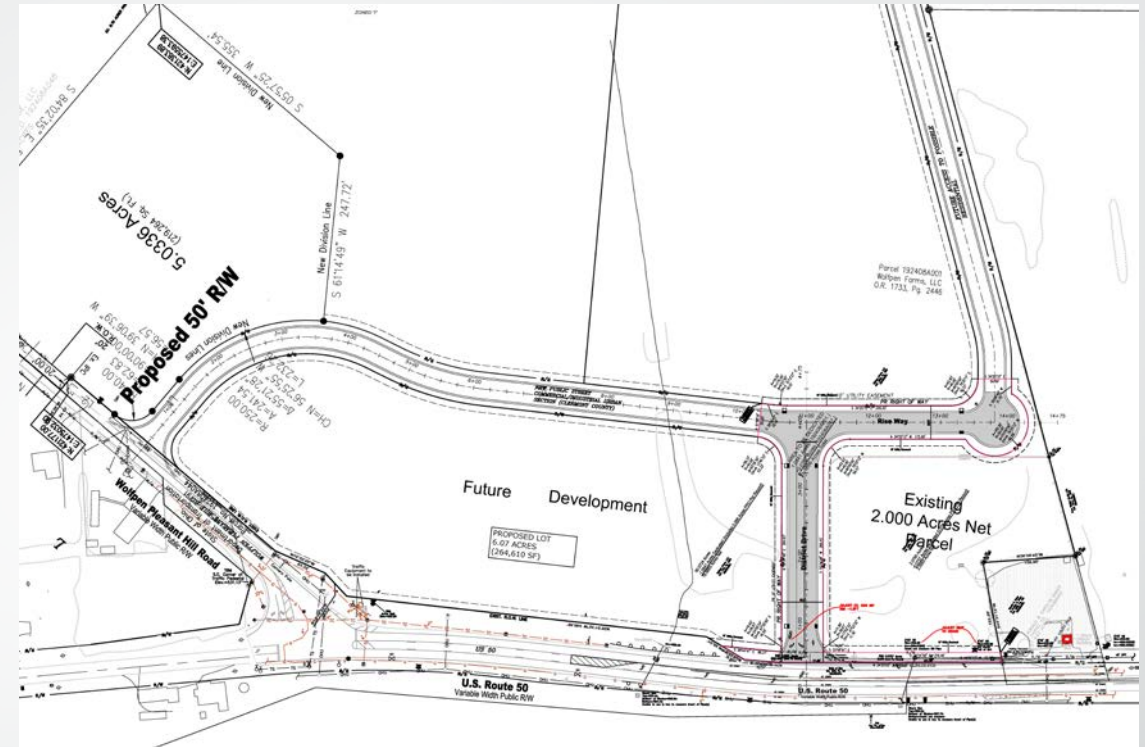

Gibson Road Bridge Replacement (T194-1.30)

- Road is now closed and Utility companies are relocating overhead
- Contractor will start bridge within the next few weeks, once utilities are moved.
- Completion estimate - 8/1/2025

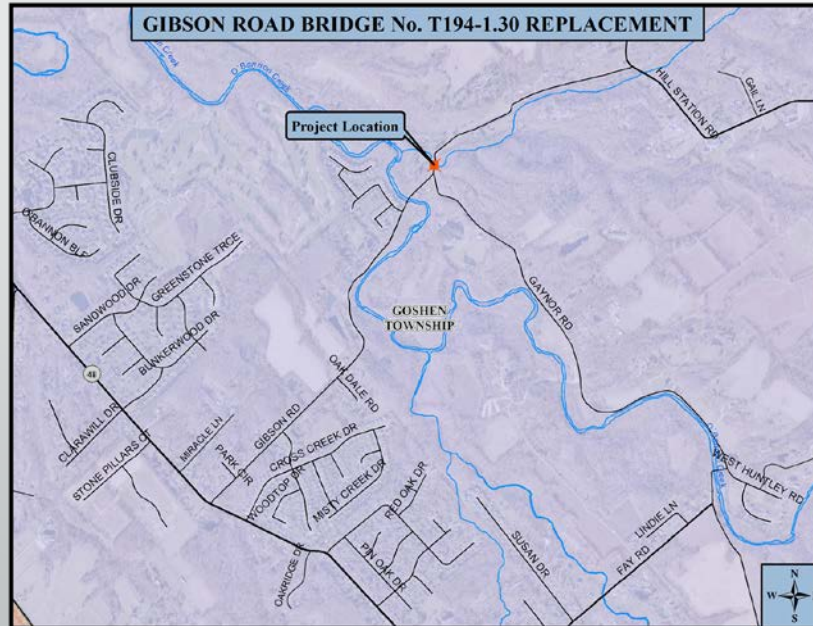


Shiloh Road Bridge Replacement (C157-2.35)

- Box in place finishing up walls and guardrail
- Completion Estimate – end of April




Bray Road Bridge Replacement (T170—1.27)

- Finishing up guardrail and asphalt
- Completion Estimate – end of April

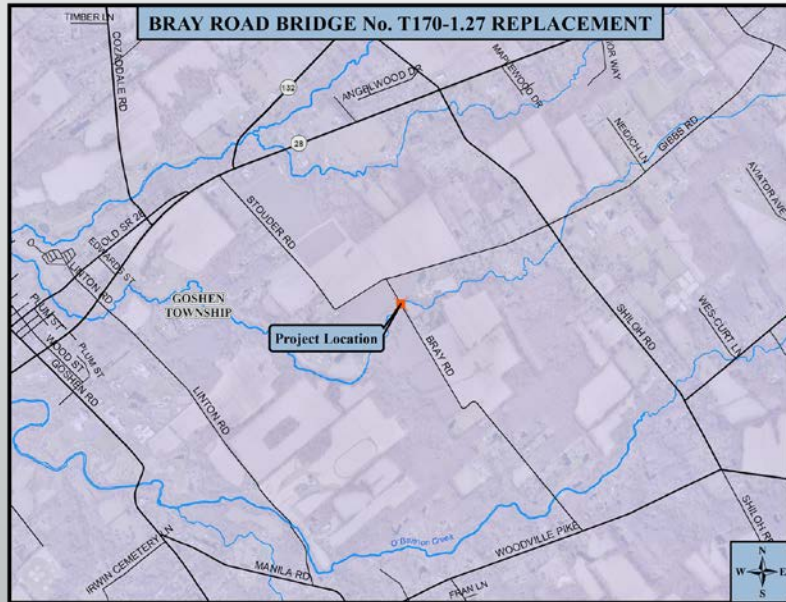


Marathon Edenton Road Bridge Replacement (C82-1.61)

- Review of final drawings and bid package
- Prepare bids in April

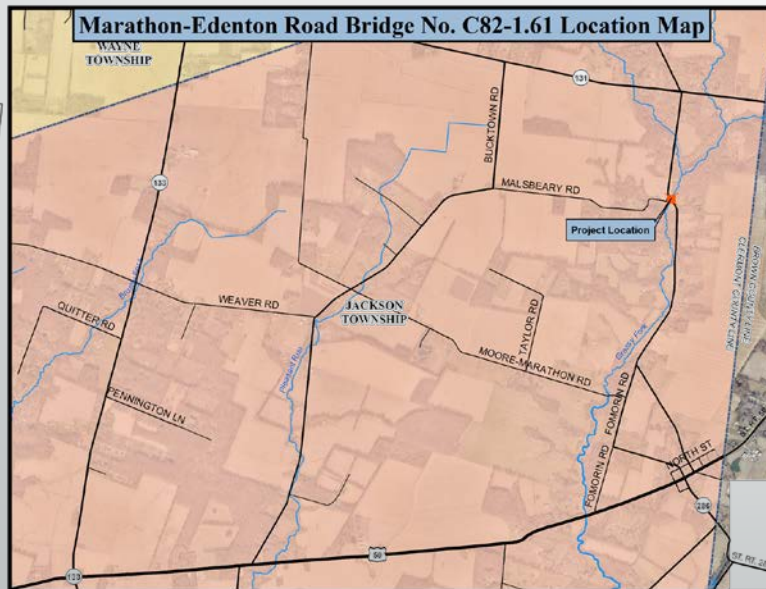



Newtonsville Hutchinson Road Bridge Replacement (C93-2.08)

- Bidding to start in April

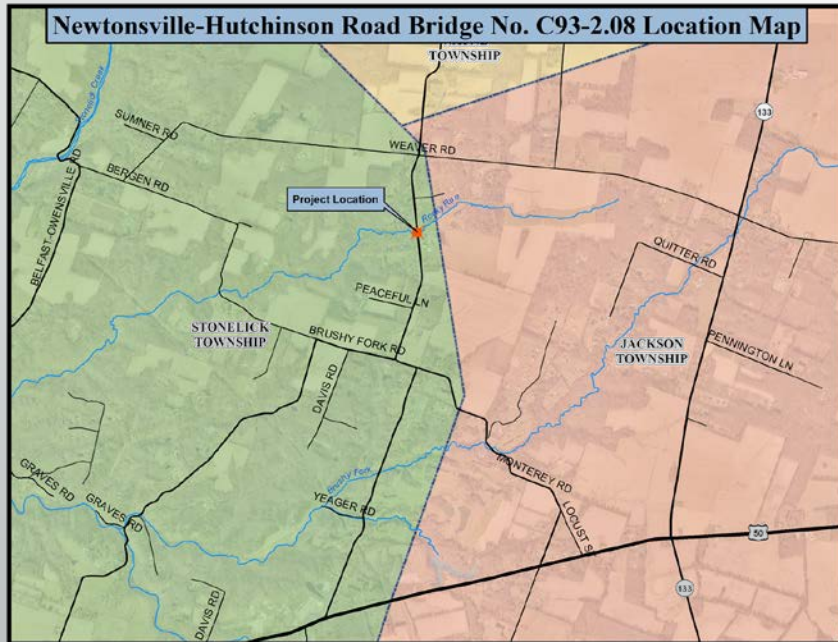


Milford Schools Roadway Improvements

- Utility meeting scheduled
- ROW Acquisition in process
- Appraisals to be complete in May

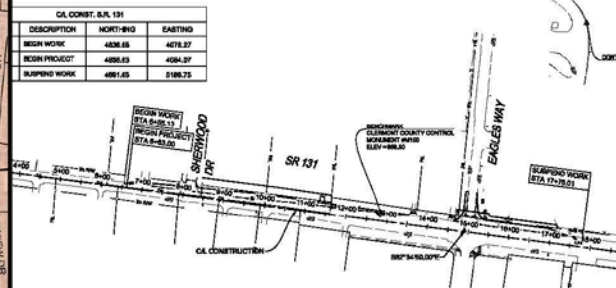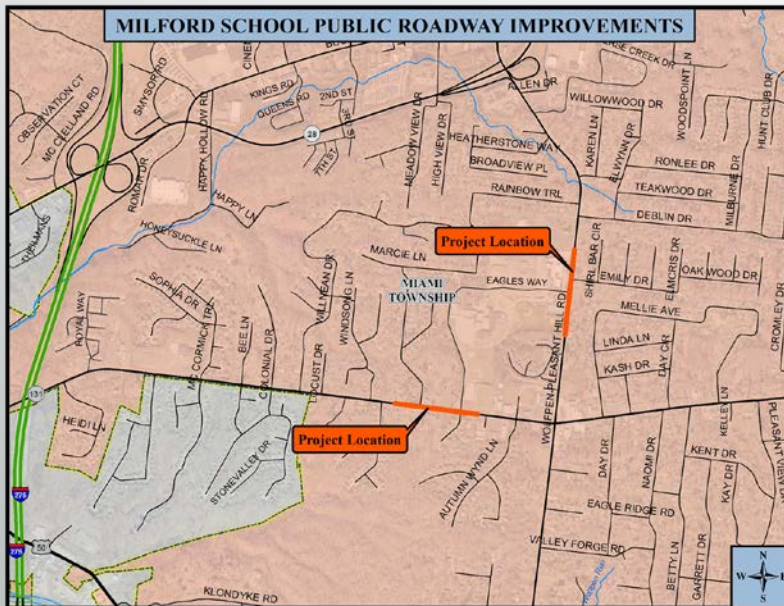

Old SR 74/Elmont Drive

- Choice One contracted for design work
- Plans to be complete July 2025

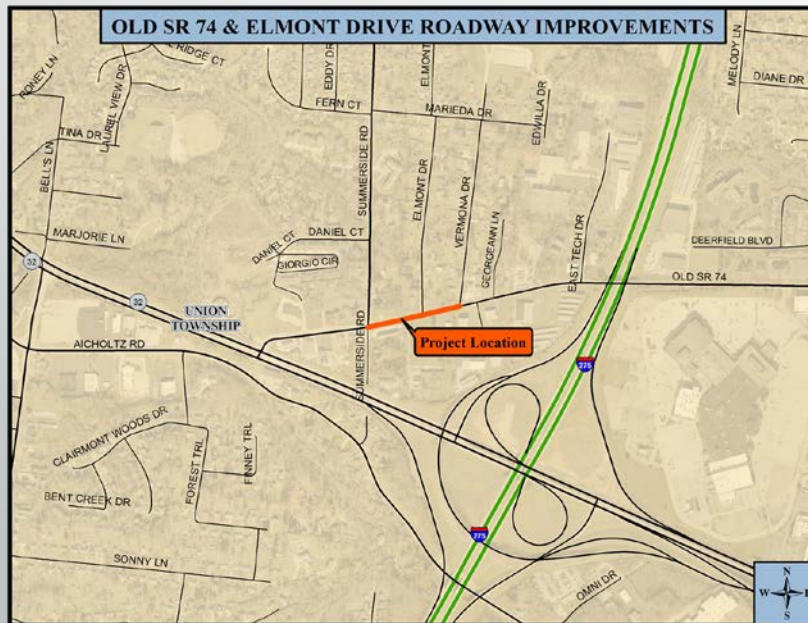

Belfast Owensville Road Bridge Replacement (C10-2.69)

- Bidding to start in April

